


# Quarterly Progress Report

January-March 2019

## Balochistan Education Project

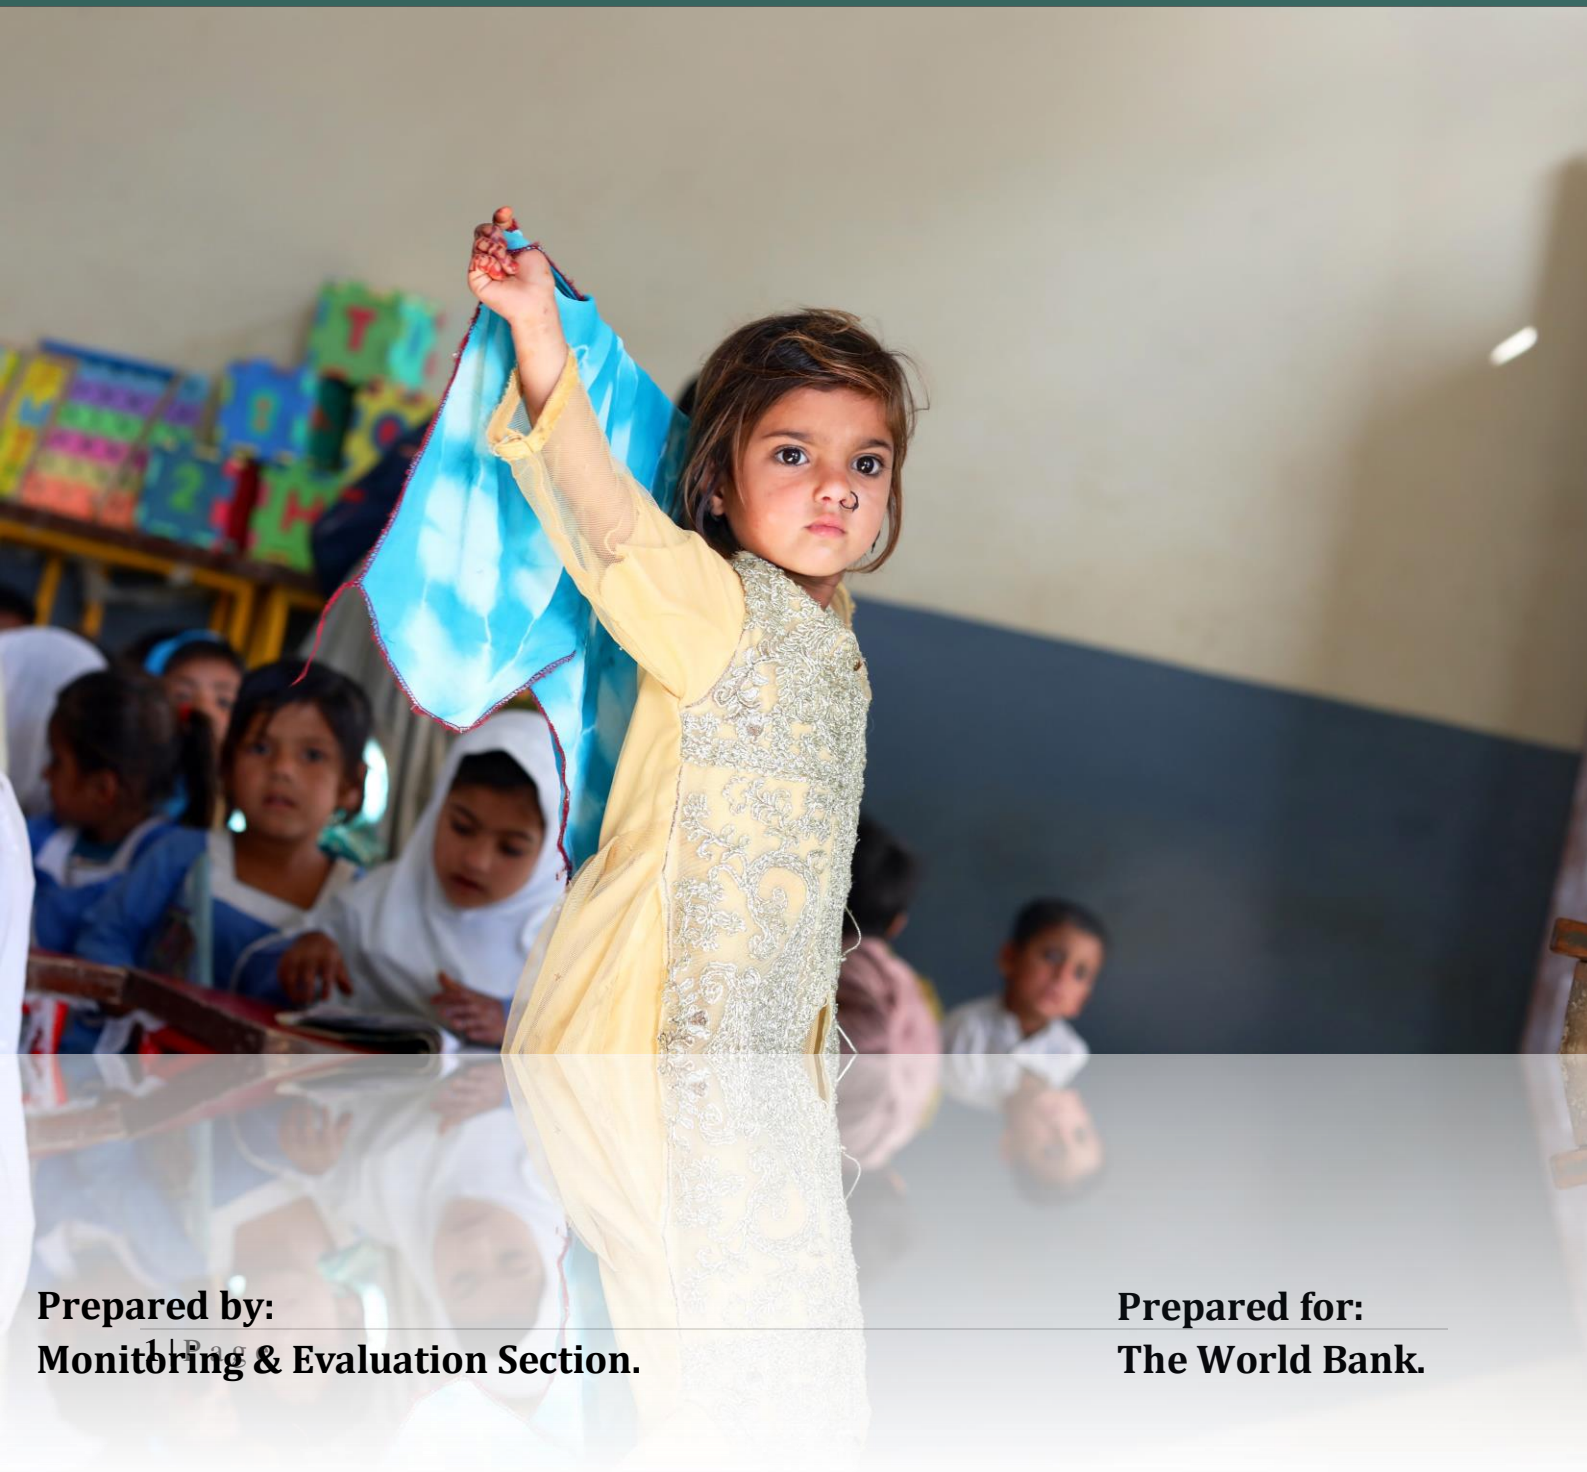

Prepared by:  
Monitoring & Evaluation Section.

Prepared for:  
The World Bank.

# CONTENTS

---

• Executive Summary	03
• Project Overview	04
• Project Development Objectives	05
• Education	13
• Development	14
• Procurement	15
• Monitoring and Evaluation	15
• Environment and Social Safeguard	15
• Human Resource	18
• Grievance Redressal Mechanism	20
	21

## Executive Summary

Project Management Unit (PMU), Global Partnership for Education-Balochistan Education Project (GPE-BEP) is implementing a three-year project under the supervision of World Bank. The PMU has identified and notified all 725 locations for new primary schools and all 95 primary schools to middle and 25 middle schools to high level for up-gradation with set notified criteria. 1,534 teachers have been recruited and deployed for 700 newly established and 120 upgradation schools. Recruitment of all the target teachers under the project is complete.

Per BEP MIS Dashboard, 1,809 (91%) total teachers have been trained against the target of 1,988 under the project. The teachers trained include the ECE teachers, EST teachers, and Head teachers of the project schools.

In the reporting period, K-5 students' total enrolment has been reported as 56,308 in 700 new established primary schools, and 120 (95 Middle and 25 High) established up-gradation schools. This enrolment achieves 133% of project total enrolment target (42,308) of K-5. The enrolment segregated gender wise makes it 38,366 of girls' enrolment and 17,942 of girls enrolment in grade K-5 in the project supported schools.

The retention of the students in the project schools has been calculated in the quarter last year .i.e. Jan-Mar, 2018. The students' retention is calculated as 81% against the project target of 75% for the project year two. The retention is calculated of 303 schools which have completed their one year study session and started the second year. The target is achieved at commendable ratio of 108%.

Furthermore, 829 total schools were advertised for construction works. Contracts have been awarded to start works in 808 schools. 767 schools completion certificates have been issued per project update dashboard whereas 57 works completion certificates are underway and shortly be issued.

Early Childhood Education-ECE kits were procured for 840 schools, in addition Taleemi Basta for ECE and Multi-grade classes was procured for all 845 schools. In the reporting period, ECE Program has been established in 820 schools including 700 newly established schools and 120 upgraded schools and 820 established schools have been provided with the TLM kits. Simultaneously, 820 established schools have been provided with the furniture including blackboard.

# Project Overview

---

The Government of Balochistan, Education Department is implementing a project titled "Global Partnership for Education-Balochistan Education Project" (GPE-BEP). The development objective of the proposed three years' project is to increase enrollment and retention in project supported schools, with a special focus on girls' participation, and to develop mechanisms to improve quality of school management.

The three major components of this project are outlined below:

## **1. Access and Equity**

a. Establishment of 725 new primary schools (Mixed Gender) with provision of early childhood education and involvement of community

b. Up-gradation of 120 schools (95 Primary to middle schools and 25 middle to higher secondary)

## **2. Quality and increased accountability**

a. Promoting Early Childhood Education through teachers training and teaching learning material.

b. School information collection, dissemination and use for improved planning and decision/Real Time School Monitoring system

## **3. Technical Assistance for improved Capacity for Management and Monitoring**


a. Teacher development through provision of Teaching and Learning Material (TLM).

b. Student Assessment

c. School Information System


# Project Development Objectives

## 1.1 Girls enrolled in grades K-5 of project supported government schools

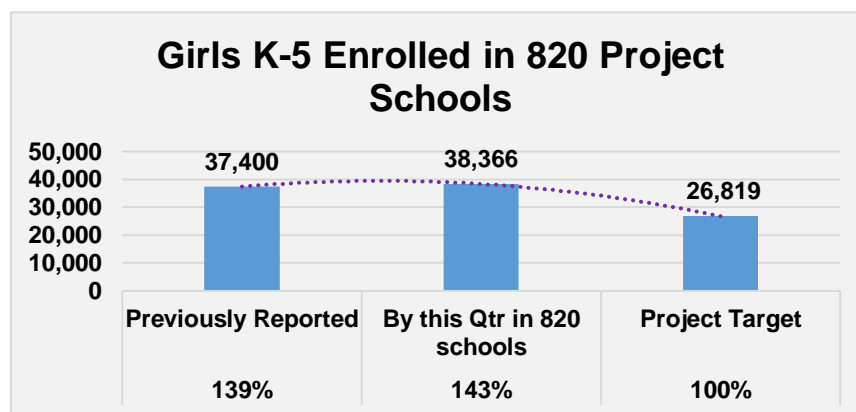


37400 is the enrollment reported before last quarter. 38366 is the enrollment reported last quarter and same is reported this quarter as no data collection has been conducted in the reporting quarter due to end of SMIPs contracts.

## 1.2 Boys enrolled in grades K-5 of project supported government schools

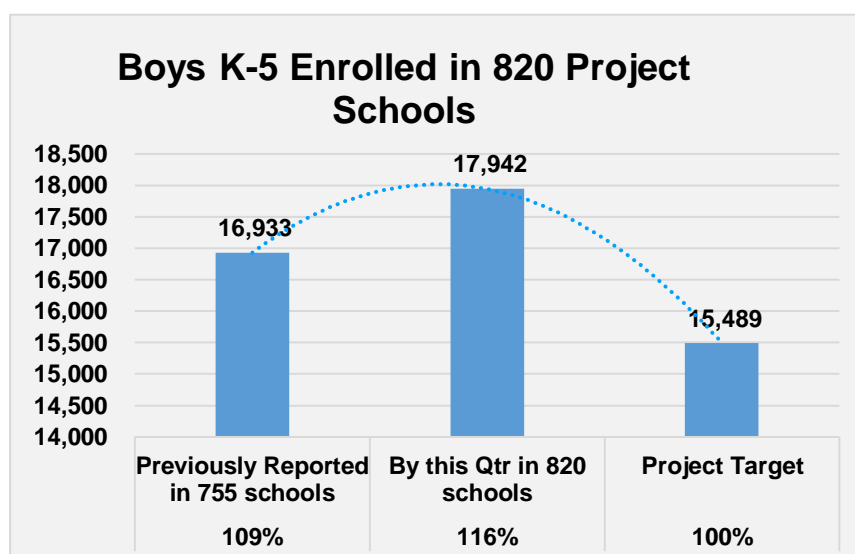

16933 is the enrollment reported before last quarter. 17942 is the enrollment reported last quarter and same is reported this quarter as no data collection has been conducted in the reporting quarter due to end of SMIPs contracts.


### 1.3 Girls enrolled in grades 6-10 of project supported government schools

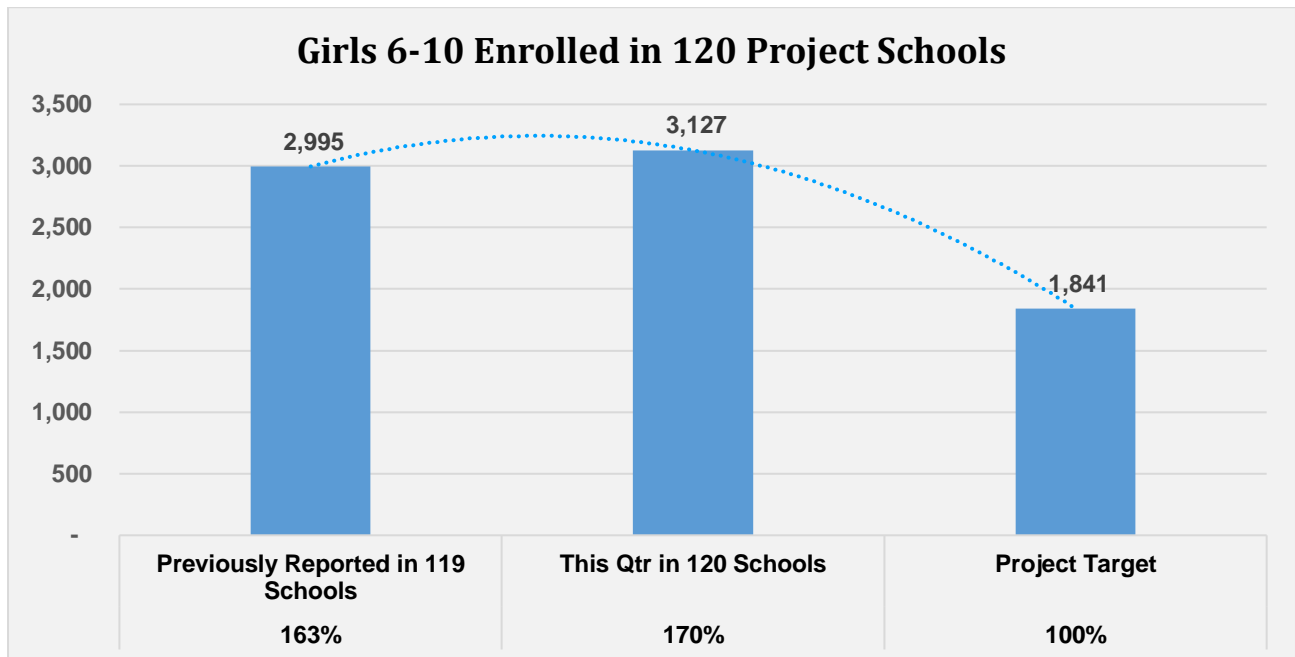

2995 is the enrollment reported before last quarter. 3127 is the enrollment reported last quarter and same is reported this quarter as no data collection has been conducted in the reporting quarter due to end of SMIPs contracts.

## 1.4 Students retention in project school


Students Retention in Project Schools for Year Two

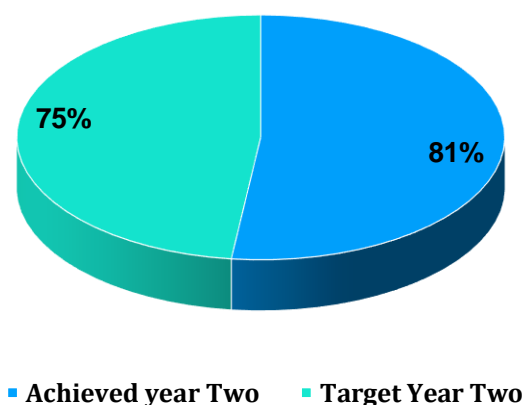

$$\frac{\text{Y2 total enrollment} - \text{Y2 total new enrollment}}{\text{Y1 total enrollment}} \times 100 = \text{Retention}$$

## 2.0. INTERMEDIATE RESULTS


### 2.1. Number of new primary schools established through community support

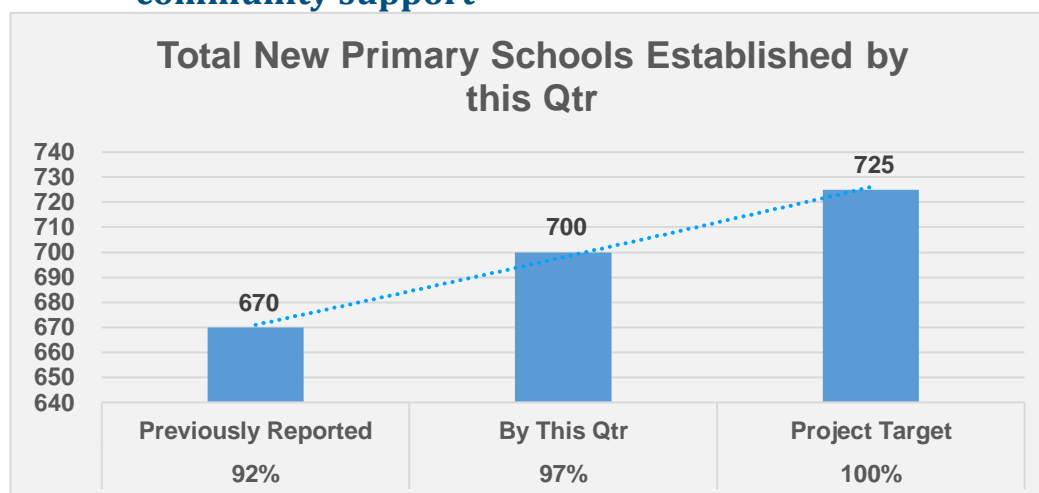

670 is the number of the schools reported last quarter. 700 is the number reported this quarter. The 30 schools which were not reported last quarter did not have any enrollment due to teachers late joining. We included the 30 schools in the 'established' portion because these schools have been provided with all the other school facilities, school supplies, school building and the teachers but only due to delay in teachers joining the school, we could not record these schools enrolment.


## 2.2. Number of schools upgraded from primary to middle level

### Total of 95 Pimary Schools Upgraded to Middle

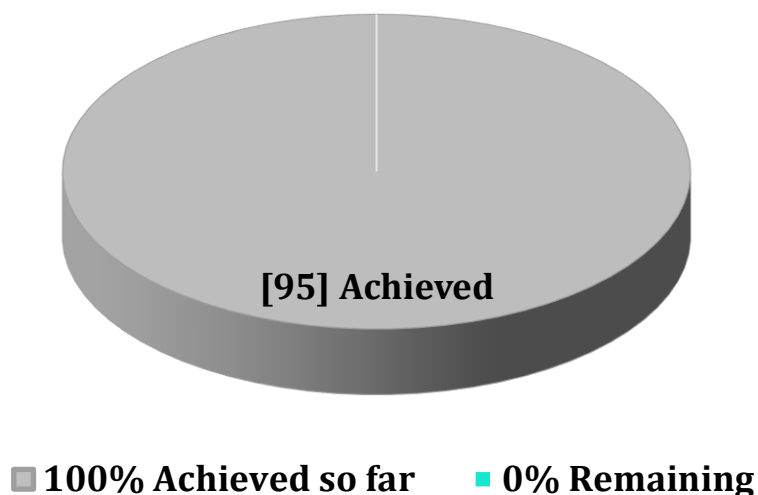

## 2.3. Number of schools upgraded from middle to high/higher secondary level

### Total of 25 Middle Schools Upgraded to High

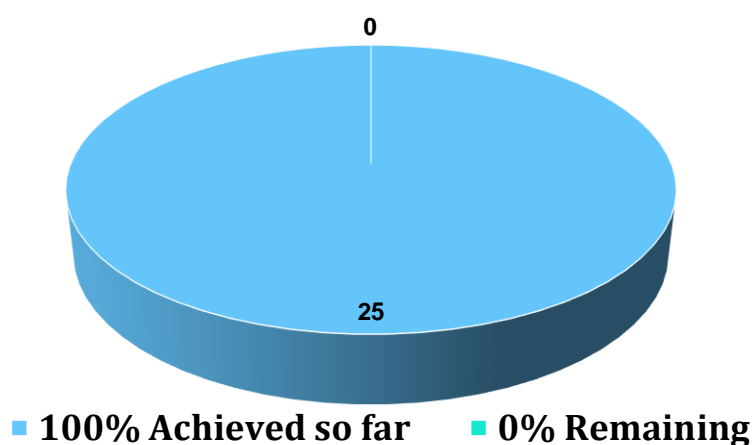



## 2.0.1. Development Works Progress by Reporting Quarter

Chart A



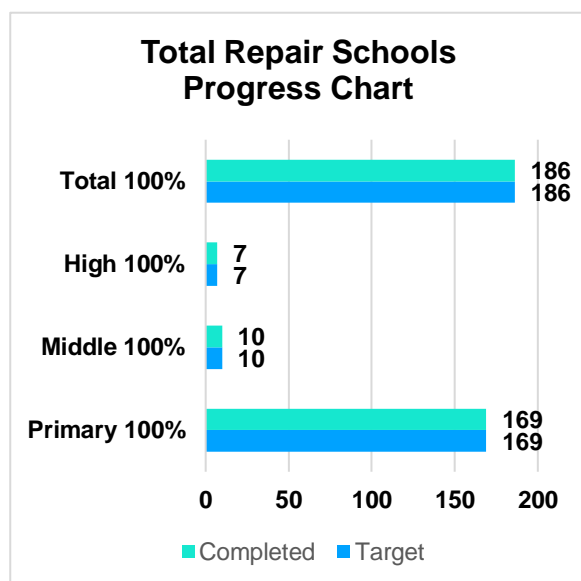


Chart B

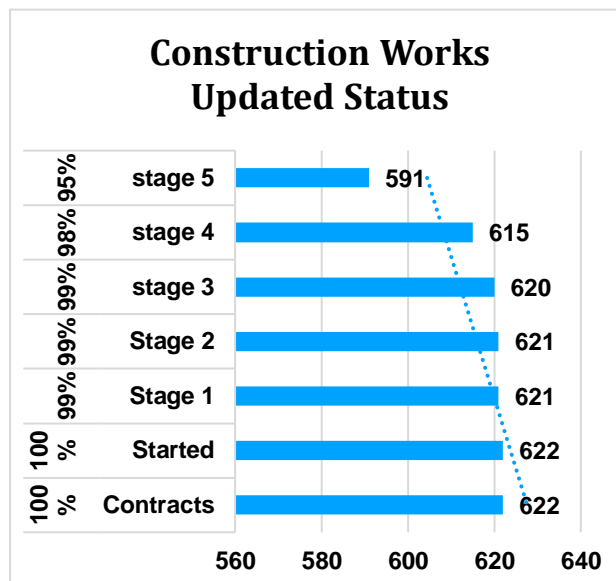


The repair schools have completed 100% works (chart A). Referring to chart B, 591 of 622 schools have completed construction works per Project update dashboard. However, this figure is around 620 per development section. Only it has not been updated on dashboard. It will shortly be updated.

## 2.4. Number of government schools to which furniture (incl blackboard) is provided

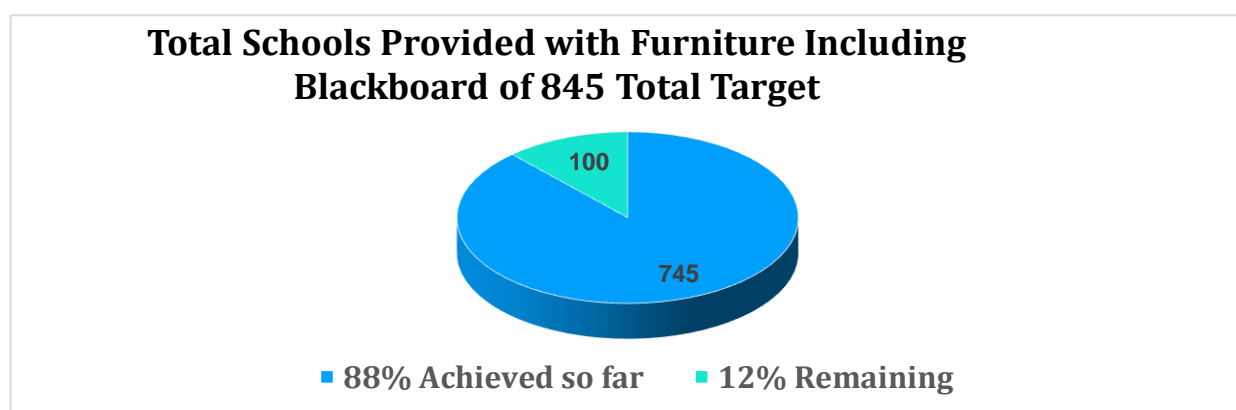


745 is the figure reported on M&E Dashboard coming through last quarter data collection. However, this quarter, referring to the evidences dashboard, all the 820 established schools have been provided with furniture including blackboard.

## 2.5. Number of schools to which TLM kits provided

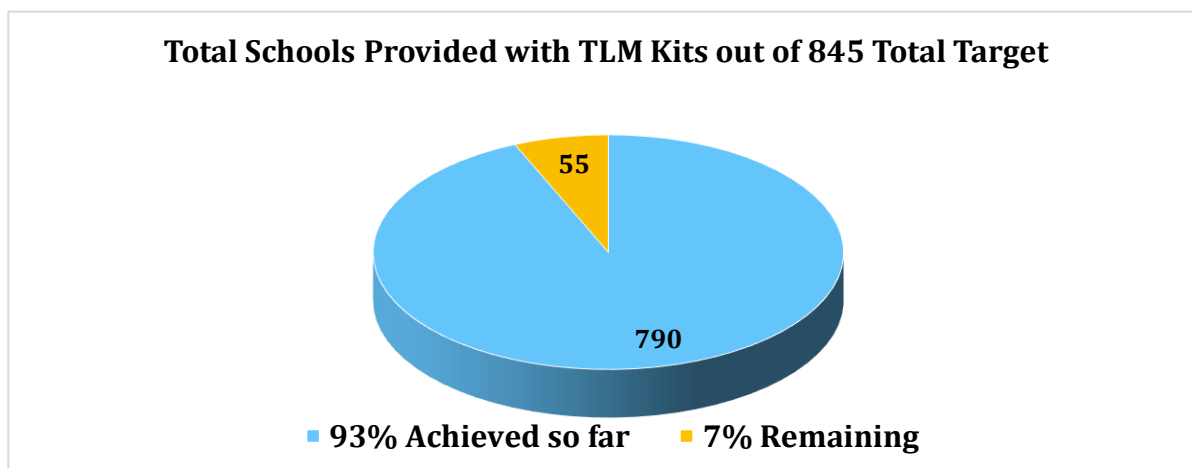


790 is the figure reported on M&E Dashboard coming through last quarter data collection. However, this quarter, referring to the evidences dashboard, all the 820 established schools have been provided with the TLM kits.

## 2.6. Number of government schools in which ECE program established

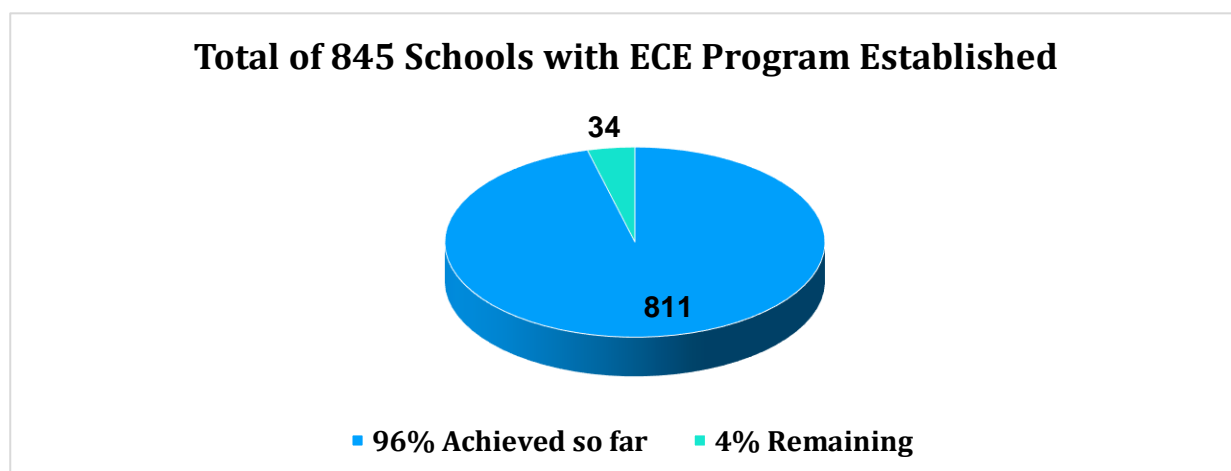


811 is the figure reported on M&E Dashboard coming through last quarter data collection. However, this quarter, referring to the evidences dashboard, all the 820 established schools have been established with ECE program.

## 2.7. Number of PTSMC members trained in targeted project schools

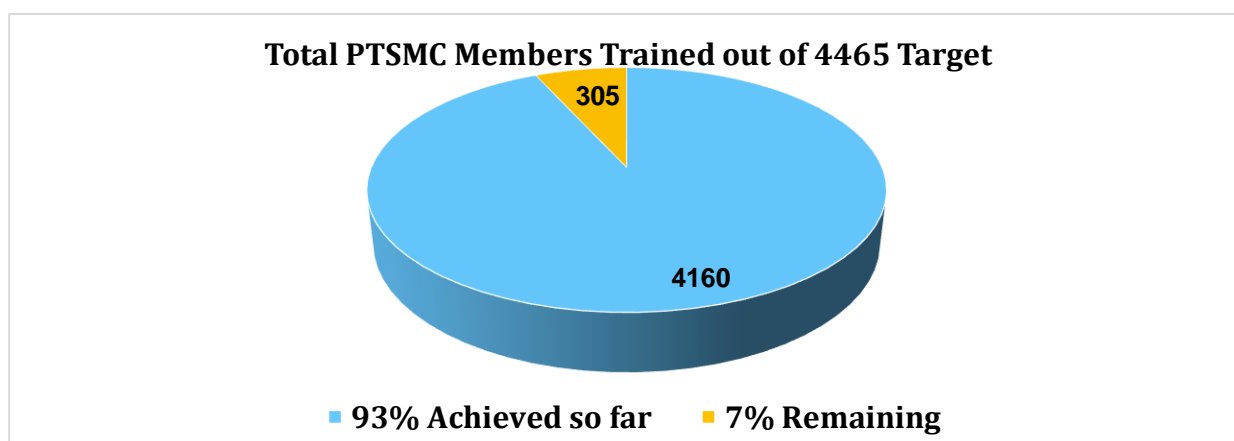

## 2.8. Number of teaching staff trained in the project specific schools

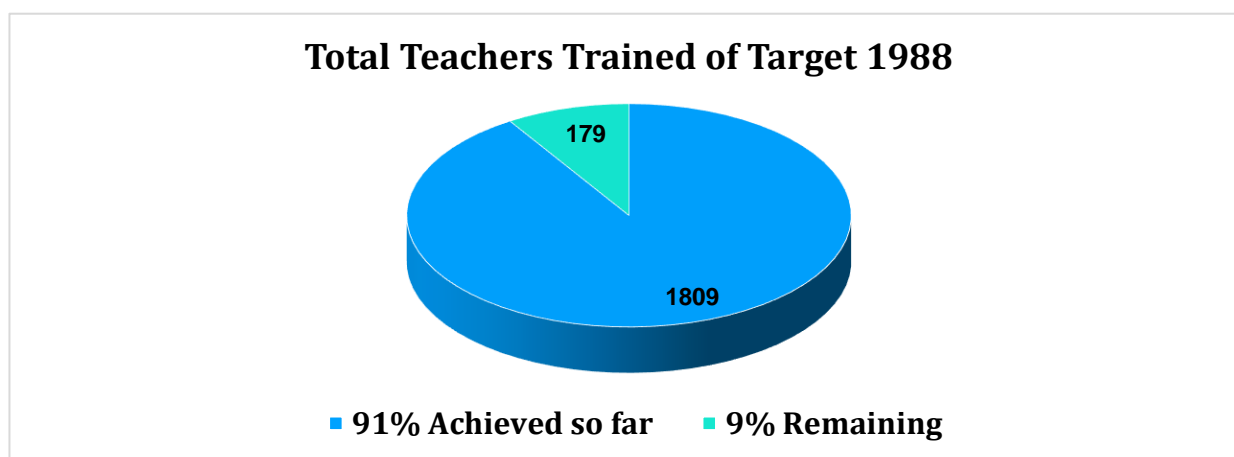

## 3.0 DETAIL TABLE OF THE SET TARGET ACHIEVEMENT AGAINST THE RESULT FRAMEWORK

Project Development Objectives	Target	Status	Remarks
Girls enrolled in grades K-5 of project supported government schools	26819	38366	143% Target achieved
Boys enrolled in grades K-5 of project supported government schools	15489	17942	116% Target Achieved
Student retention in project schools	75%	81%	108% Target Achieved ( the target has been calculated as of year two though these 303 schools have completed their first study session)
Girls enrolled in grades 6-10 of project supported government schools	1841	3127	170% Target Achieved

## Intermediate Results

Number of new primary schools established through community support	725	700	97% Target Achieved
Number of schools upgraded from primary to middle level	95	95	100% Target Achieved
Number of schools upgraded from middle to high/higher secondary level	25	25	100% Target Achieved
Number of government schools to which furniture (incl blackboard) is provided	845	745	97% Target Achieved
Number of schools to which TLM kits provided	845	820	97% Target Achieved
Number of government schools in which ECE program established	845	820	97% Target Achieved
Number of PTSMC members trained in targeted project schools	4465	4160	93% Target Achieved
Number of teaching staff trained in the project specific schools	1988	1809	90% Target Achieved
Project reports generated on selected indicators	11	11	100% Target Achieved

## **1.Social Mobilization and Implementation Partner (SMIP)**

Review and Lesson Learned workshop organized at Karachi where District Focal Persons (DFPs) and SMIPs participated to share their progress and learning during the implementation of Balochistan Education Project.

## **2.Entry of BEP schools in EMIS data**

BEP schools are allotted with the BEMIS codes in 2018. A detailed information as per EMIS software is needed from each schools in hard with proper verification to include BEP schools in NEMIS for the current Census. This information was collected from 593 schools and timely entered in the software.

## **3.Completion of ECE Baseline & learning assessment activity**

ECE baseline and learning assessment is conducted in 66 sample schools from 17 randomly selected districts. Total 990 students were assessed on the defined tools developed on 3 subjects English, Mathematics and Urdu in reference to ECE curriculum 2007. Results shows that overall performance of the students assessed is 65%.

ECE Baseline and assessment result dissemination seminar was organized by BEAC where all the stakeholders' representative from Directorate of Education, PPIU, PITE, Teachers, and UNICEF participated.

## **4.Compilation of Teacher training data:**

During the project period around 1800 teachers were trained successfully through PITE. All the trained teachers' information was compiled in soft through attendance sheet and Teacher information forms.

## **5.Finalization of EU schools list for project implementation:**

List of schools for implementation of EU – BES project activities was finalized through coordination with district education authorities during a consultative workshop. But due to duplication of schools for up-gradation in PSDP, some schools were revisited and the list was re-verified by education authorities.

## **6.Updated BEP & EU dashboard:**

Hard and soft data pertaining to Education section is updated on dashboard

## **7. Planning for EU project implementation strategies and budget finalization against each planned activity.**

## **8. Process final settlement of SMIPs, DFPs & PITE**

**9. BEP case for teacher regularization and SNE moved to education department.**

**10. Planning for Cluster head teachers training**

**11. Finalization of cluster head teachers training module in consultation with resource persons.**

## Development and Infrastructure

The Development and Infrastructure section of the project management unit had to develop 845 schools with the segregation of numbers 725 primary schools, 95 middle level schools, 25 high schools. The targeted developments in the schools through the section were related to the infrastructure needs. The infrastructure needs were identified through the baseline survey and technical validation of each school. The priorities set were the construction and development of classrooms, ECE room, veranda, courtyard, pathways, a set of dry pit latrine, water storage tank, water taps, and planters. Special arrangements for differently able children, i.e. ramps, hand rails, and planters.

The development section has achieved the target of developing and constructing of all the primary, middle, and high schools which were complete and these completed schools are already handed over to the secondary education department and are functional in all respect. The remaining primary 66, middle 10 and high 5 schools are in progress for handing over to the education department and the process would be completed by 30<sup>th</sup> of May 2019 and will be functionalized accordingly.

# Procurement

Following activities have been carried out during the last quarter under procurement;

1. 50 High schools were provided state of the art quality sports goods throughout Balochistan to promote healthy environment and inter-school competition.
2. 31 High schools were provided 10 laptops each school to promote IT awareness and educational promotion activities.
3. All the pending Works contracts requiring time extension and variations were processed.
4. Procurement of additional Furniture, Science Lab. Equipment and Teachers Learning Material (TLM) was planned by utilizing Fx-Gain.
5. Contracts for Goods (Supply of Furniture) was extended to cover the Fx-Gain procurement.
6. Annual Warehouse Reconciliations were performed along with physical stock count.
7. Transformation of warehousing responsibilities from Procurement Section to Admin Section.

## Monitoring and Evaluation

### M&E Tasks

#### Field Monitoring Visits

Conducted various field visits to District Sibi, Gawadar, and Qilla Abdllah for monitoring schools supply and construction works progress. The findings were shared with the management for the follow and immediate actions.

#### BEP Schools Profiling in Hard and Soft format

M&E section has been regularly supervising updating of all the 845 schools profiling in hard and soft formats. Over 95% of all the hard and soft school profiles have been completed. The remaining 5% will shortly be completed. All the hard profiles are set in the racks at M&E sections under the supervision of M&E Officers. The soft profiles have been updated on Schools Profiling Dashboard and can be accessed by anyone around the globe.

### **Status of Evidences on Dashboard**

M&E Section has regularly been checking all the evidences over the evidences MIS dashboard and has been intimating the discrepancies to the concerned officers for improvement.

### **BEP Procurement of Goods-A study**

The objective of this report was to study the goods procurement process from Tender, Delivery, Release to Supply and any critical findings/limitations/corrective measures for future goods procurement under PMU projects.

All the data on the GRNs uploaded on dashboard matched the data on the GRN record and dynamic excel sheet with procurement section though there was some data which was not reflected on the Dashboard completely due to the excessive number of GRNs and all cannot be uploaded to the MIS dashboard. It was found that the GRNs uploaded on the dashboard were not complete and uploading all GRNs is not possible as one school has at least 15 GRNs or more.

The dynamic excel sheet created by Procurement team was an excellent record sheet and a lot of efforts were put in creating it. Everything from tenders' record to school supplies to GRNs and financials etc. were punched in it.

### **Qualitative Study over BEP Interventions**

BEP M&E section carried out a qualitative study to incorporate lessons learnt for future intervention and to record the perception of stakeholders about BEP intervention.

BEP team opted purposive sampling technique to gather qualitative data from summer zone schools. Teachers, students, District authorities and PTSMC members were interviewed using data collection tools i.e. Key Informant Interviews, Focus Group Discussions & Semis Structure Interviews.

Data was collected from 8 districts of summer zone. Total 17 schools were visited during this time period and qualitative data was collected from stakeholders.

### **Developed EU BES Baseline Analysis Plan and MIS Dashboard**

M&E section developed EU BES schools baseline analysis plan and shared with all the concerned sections for review and feedback. The analysis plan was finalized and shared with the IT/MIS section for development of the EU BES Baseline Analysis Dashboard. The dashboard is ready now with the display of all the key indicators on main page.

### **EU BES Schools Baseline Raw Data Analysis/Overview**

M&E section conducted EU Schools Baseline Raw Data Analysis and Overview and shared with Education section for their feedback and improvement in the data. Later, the meeting was conducted between M&E and Education sections where all the findings were discussed and the data was worked out for corrections of some mechanical errors. The data is now cleaned and available for presentation.

### **Way forward**

M&E Section, in following quarter, will initiate/develop M&E Framework, M&E Plan, M&E tools, M&E application for data collection, M&E Analysis Plan, M&E SOP, and M&E Dashboard for BES Project. All these important tools and dashboards will be developed in regular coordination and consultation with the Education, Development and Procurement Sections.



## **Media and Communication Tasks**

Media and communication section has thoroughly remained vibrant during the quarter and the following major task were completed.

- Development, publishing and dissemination of Project Newsletter.
- Development of Audio Video Presentation.
- Development of Project Documentary.
- Managing Enrolment Campaign through various social media platform.

## **MIS/IT Tasks**

### **Procurement System Development**

MIS Section has automated the procurement system by developing online procurement plan for Goods, in which we track each procurement tasks steps, status, progress with evidences w.r.t World Bank guidelines. System can auto alert before or near contract expiry date.

### **MIS-Evidences System**

Designed and developed user interface for images uploading and verification mechanism.

### **Deployment of MIS on Cloud**

We have deployed our whole MIS system from local setup to Cloud at <http://mis.bep.org.pk>.

## **EU Baseline**

Developed EU baseline module for EU selected 100 potential schools, 100 feeder and 100 next level schools. Analysis and reporting against each EU school. Auto generated raw data of EU schools

### **Dashboard Development of EU Baseline**

MIS section has integrated EU project with MIS system by separate user interface and user level access for end users.

## **MIS Maintenance**

MIS Section has maintained MIS modules related to each section as M&E, Development, Education, Finance and Procurement and delivers the required data to them.

## **E-Learning**

MIS team along with Education Specialist visited Panjab IT board to explore the activities related to E-Learn and work, and to learn how to implement same model in Govt schools of Balochistan.

# Environment & Social Safeguard

Data of all the 845-siting stage has been collected, reported and updated on MIS dash board. By the end of 2018 data of 676 checklist of construction stage were collected reported and updated on MIS dashboard. Total 79 construction stage checklists data have been received during first quarter of 2019. As per the data collected no environmental or social issue was reported.

S.No	District	Total schools per district	Consolidated data of construction stage checklists received during previous quarters	Construction stage data received during first quarter,2019	Key findings	Remedial measures taken
1	Quetta	27	23	0	No environmental or social issue reported	
2	Pishin	30	23	6	No environmental or social issue reported	
3	Mastung	19	18	0	No environmental or social issue reported	
4	Killa Abdullah	38	33	0	No environmental or social issue reported	
5	Khuzdar	34	24	9	No environmental or social issue reported	
6	Kalat	10	8	0	No environmental or social issue reported	
7	Sakindara nad	13	12	0	No environmental or social issue reported	
8	Lasbela	47	44	1	No environmental or social issue reported	
9	Awaran	20	13	7	No environmental or social issue reported	
10	Zhob	35	29	2	No environmental or social issue reported	
11	Sherani	20	15	0	No environmental or social issue reported	
12	Harnei	20	18	0	No environmental or social issue reported	
13	Ziarat	26	22	0	No environmental or social issue reported	
14	Killa Saifullah	36	34	0	No environmental or social issue reported	

<b>15</b>	Loralai	19	13	4	No environmental or social issue reported	
<b>16</b>	Kohlu	16	15	0	No environmental or social issue reported	
<b>17</b>	Barkhan	29	25	4	No environmental or social issue reported	
<b>18</b>	Musakhail	27	21	6	No environmental or social issue reported	
<b>19</b>	Duki	12	10	0	No environmental or social issue reported	
<b>20</b>	Sibi	19	8	2	No environmental or social issue reported	
<b>21</b>	Jafferabad	28	28	0	No environmental or social issue reported	
<b>22</b>	Dera Bugti	32	11	8	No environmental or social issue reported	
<b>23</b>	Jhal Magsi	20	20	0	No environmental or social issue reported	
<b>24</b>	Naseerabad	46	46	0	No environmental or social issue reported	
<b>25</b>	Kachi	20	12	3	No environmental or social issue reported	
<b>26</b>	Sohbat Pur	28	28	0	No environmental or social issue reported	
<b>27</b>	Noshki	25	22	0	No environmental or social issue reported	
<b>28</b>	Chahgi	30	25	5	No environmental or social issue reported	
<b>29</b>	Washuk	19	17	0	No environmental or social issue reported	
<b>30</b>	Kharan	29	22	6	No environmental or social issue reported	
<b>31</b>	Panjgoor	21	16	0	No environmental or social issue reported	
<b>32</b>	Gwadar	24	9	9	No environmental or social issue reported	
<b>33</b>	Kech	26	12	7	No environmental or social issue reported	

## **I) PROGRESS UPDATE**

The project commenced in July 2015. This report highlights the activities of the quarter January to March 2019 covering the overall activities from January 2019 – March 2019.

Human Resource Section in GPE-BEP is providing multi-layer support to GPE-BEP project. The Project is now at the critical stage of completion and Human Resource Department through competitive recruitment, facilitation and support to program is contributing its share towards the successful completion of the project.

Following are the key highlights of the achievement made by Human Resource Section in the 1<sup>st</sup> Quarter of 2019.

### **Staff Strength & Status**

Critical Positions like Manager Finance, Human Resource Officer, two School Development Engineers, Media and Communication Officer, two Program Associates and two assistant positions were hired through the recruitment process enlist in the guidelines. Finding good Human Resource especially at the ending phase of the project is always a difficult task but the above positions were filled well due in time with the best candidates available in the market.

HR Section prepared & issued contract Extension addendum for the year 2019. The period covered under these addendum was from January 2019 till March 2019.

Employee Personnel files of GPE-BEP staff are maintained and up to date.

HR Section finalized the performance appraisal for the year 2018 and implemented the decisions of competent authority.

Human Resource Section always focused on timely disbursement of Payroll in the 1<sup>st</sup> Quarter, beside the challenges of changing signatories, the salaries of the 1<sup>st</sup> quarter were release on time.

Human Resource Section played active role in departmental transitions of the Project Directors, in the 1<sup>st</sup> Quarter of 2019 our new Project Director joined the Office and HR supported in smooth transition and process by providing organizational memory on critical occasion and asked by the Project Director. HR Section also acquire important NOL from World Bank such as appointment of Project Director.

In the 1<sup>st</sup> quarter of 2019, Several Staff wellness activities were planned and executed by HR Section. That includes celebration over the marriage / Nikkah of a staff member, HR Section also organized farewell of Manager Education.

HR Section provided support in leave and attendance mechanism and provide timely information to higher management and Staff.

HR Section responded to different grievances raised on the grievance mechanism of World Bank, Secondary Education Department, all complaints have been handled professionally and closed with satisfactory responses.

# Grievance Redressal Mechanism

## GRIEVANCE REDRESSAL MECHANISM (GRM):

Summary of BEP-GRM Cases						
Description	Cases by Oct-Dec, 2018			Cases by Jan-Mar, 2019		
	Total Filed	Total Disposed of	Total Pending	Total Filed	Total Disposed of	Total Pending
*CRC/General Complaints	50	50	0	50	50	0
Court Cases	36	16	20	36	16	20
Procurement Cases	5	5	0	5	5	0
<b>Total</b>	<b>91</b>	<b>71</b>	<b>20</b>	<b>91</b>	<b>71</b>	<b>20</b>

*\*CRC/General Complaints include all the complaints submitted to confirm schools selection, NTS tests, and Teachers selection. Since CRC-Complaint Redress Cell is chaired by concerned division honorable Commissioner at Division level, PMU does not have any mandate to redress the cases falling under the CRC level specifically in regard to teachers selection. However, PMU GRM-PAC receives the complaints and guides the complainants to move to the CRC to file their complaint.*

**Balochistan Education Project (BEP ) Grievance Redressal Sheet by Jan-Mar, 2019**

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	03-Jan-16	Jamila Hassan	Nawa Kili Quetta 0304-3324241	Complaint application was submitted regarding NTS merit list UC Nawa kili	–	Yes	Complainant wanted to exclude ADE marks of qualified candidate. Her request was rejected by District Recruitment Committee as not valid. In recruitment policy issued by Education Department, ADE marks is applicable.	It is against Recruitment Policy notified by Education Department
2	02 - May - 16	Sain Dad	Sohbatpur Ghot Sain Dad kandani	Submission of letter (Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list.	03-05-16	Yes	The complainant wanted District Recruitment Committee to consider her candidate in lieu of provision of land. However, the Recruitment in the project is made through merit based recruitment policy as notified by Education Department. Therefore, complaint was rejected and recruitment is made on merit based only.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
3	2nd May-2016	Wali Dad	Qaisarabad Sohbatpur 0343-3788221	Complaint application was subjected regarding unfair recruitment of teacher, for he has devoted land for school and wants his candidate to be short-listed for his UC.	2nd May-2016	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
4	22-Jun-16	Bilqees D/o Nabi Dad	Lasbela UC Liyari	(JVT complain application was submitted) Complain application was regarding discrimination objection on NTS criteria	22-06-16	Yes	Applicant was ineligible because she is not Intermediate pass(which is basic qualifying criteria for teachers) and also she didn't qualify NTS test.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
5	22-Jun-16	Maryam D/o Muhammad Siddique	Lasbela UC Uthal	(JVT complain application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted.	22-06-16	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
6	22-Jun-16	Rehana D/o Yar Muhammad	Lasbela UC Uthal	(JVT complain application was submitted) In application it is stated that the community had devoted land for school on one condition iff their candidate be shortlisted.	23-06-16	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
7	24-Jun-16	Sumaira D/o Abdul Hakim	Lasbela UC Winder	Complain application was regarding discreamentative objection on NTS criteria	24-06-16	Yes	–	Applicant was not eligible because she is not FA and also she didn't qualified NTS test.
8	25-Jun-16	Samiya Khair D/o Khair Muhammad	Rehmdwa Noshki	(JVT complain application was submitted). Objection on merit list finalized by District Recruitment Committee.	07-07-16	Yes	District Recruitment Committee considered her request and issue is resolved.	–
9	26-Jun-16	Saima D/o Din Muhammad	Lasbela UC Lakhara	(JVT complain application was submitted ) she claims though she has done metriculation but is not shortlisted in NTS merit list.	26-06-16	Yes	Required qualification intermediate. She is matriculate thus District Recruitment Committee rejected her complaint.	Applicant was not eligible as per approved criteria

10	27-Jun-16	Saqiba D/o Abdul Razzaq	Loralai UC Zingewal Kotazai	(JVT complain application was submitted). Complain was stated regarding rectification of UC	24-11-16	Yes	District Recruitment Committee has verified the documents of candidates and issue was resolved	—
11	28-Jun-16	Raj Bibi D/o Muhammad Ali	Lasbela UC Uthal	(JVT complain application form was submitted) She claimed that her B.Ed and M.A degree was not considered while finalizing NTS merit list.	05-07-16	Yes	District Recruitment Committee Lasbela considered her application and it was resolved on merit. She is on 7th number in merit	—
12	28-Jun-16	Mehbooba D/o Paidar Khan 0334-2811516	Kili Saghri Loralai.	Mrs. Mehbooba complaints, that she has secured 50 marks whereas in merit list she has given only 43 marks.	24-11-16	Yes	Issue resolved by District Recruitment Committee, on the basis of complaint merit list were checked and made correction in the numbers of the complainant.	—
13	29-Jun-16	Sakina Bibi D/o Aziz Khan	Loralai UC Zangewal	Mrs. Sakina bibi complained that she has passed NTS test but her name is missing in merit list.	24-11-16	Yes	Issue is resolved, as on the basis of her complaint the merit list was tallied and found that her name was missing due to non-availability of her documents, but on submission/presentation of complete documents her name was included in revised merit list.	—
14	30-Jun-16	Razai Taj D/o Abdul Ghani	Loralai UC Ponga	C.T and B.A marks were not included in NTS merit result.	24-11-16	Yes	Case was forwarded to District Recruitment Committee and requested to include her CT and BA Marks, District Recruitment Committee verified her documents and included her marks in the merit list.	—
15	04-Jul-16	Razia D/o Yar Muhammad	Lasbela UC Winder	The candidate has declared the test and is rejected for her qualification is metric and other candidate from other UC is selected.	15-07-16	Yes	She is Matriculate only and does not meet eligibility criteria and therefore was not shortlisted and if no candidate is selected on UC level then on tehsil level candidate will be selected.	Required qualification for JVT post is intermediate with 2nd division.
16	04-Jul-16	Gul Bushra Kakar D/o Abdul Ghafor	Loralai UC Ponga	(JVT complain application was submitted) B.A and ADE marks not included	01-11-16	Yes	Issue resolved by District Recruitment Committee, the case was forwarded to District Recruitment Committee and requested to include her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract.	—

17	07-Jul-16	Hameeda D/o Muhammad Farooq	Lorlai UC Ponga	Complain was stated regarding rectification of UC	24-11-16	Yes	Issue resolved by District Recruitment Committee, On the basis of her complaint, Locals of other candidates were checked and found that on candidate were not belonging to here UC and excluded all the candidates from merit list who were not belonging to the same UC.	—
18	11-Jul-16	Shahida D/o Jumma Khan	Lasbela UC Wayara	(JVT application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted and a candidate from other UC is shotlisted.	21-07-16	Yes	Firstly she did not pass NTS test secondly if no candidate is selected on UC level then on tehsil level candidate will be selected.	District Recruitment Committee rejected the complaint because it is not in recruitment policy
19	29-Jul-16	Gulshan W/o Noorullah	Lorlai UC Thal	Higher education marks are not included in NTS merit list.	25-11-16	Yes	Issue resolved by District Recruitment Committee , the case was forwarded to District Recruitment Committee and requested to included her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract.	—
20	01-Oct-16	Khan Meer	Zhob UC Wala Akram	The UC topper Ms.Farzana Zareef does not belong to UC Wala Akram but to UC Omzha( Rectification of U.C)	14-10-16	Yes	Case resolved by District Recruitment Committee on 24-Dec-2016,	—
21	01-Nov-16	Gulshan Bibi D/o Abdul Khaliq	Qila Saifullah UC Sadar Muslim bagh	It was stated in complain that her B.Ed marks were not included in merit list.	01-12-16	Yes	Issue was addressed to District Recruitment Committee. Marks added as per documents provided	—
22	01-Nov-16	Fatima Bibi D/o Hassan Khan	Qila Saifullah UC Bandad Mir zai	Complain was stated regarding rectification of UC	01-12-16	Yes	UC Rectified by District Recruitment Committee as per documents	—
23	01-Nov-16	Zarina Kakar	Qila Saifullah UC Sadar Muslim Bagh	Objection on ADE marks seperately.	01-12-16	Yes	Issue was addressed by District Recruitment Committee.	—
24	03-Nov-16	Binish Kanwal	Quetta ,Kechi Baig	Complaint for JV teacher's recruitment. She claimed her name is not included in merit list.	3rd Nov-2016	Yes	Ms.Binish Kawal is included in merit list on 78th number , her total obtained marks are 57.25, her basic qualification is B.A because her F.A was scored in 3rd div.	—
25	03-Nov-16	Fatima D/o Pehlwan	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated for her B.A marks were not included in NTS merit result.	01-12-16	Yes	Issue was addressed to District Recruitment Committee. Marks added as per documents provided	—
26	04-Nov-16	Sadiqa D/o Nadir Khan	Qila Saifullah UC Sadar Muslim Bagh	B.Ed and Physical education marks are not included in NTS merit result.	04-11-16	Yes	Issue was adressed to District Recruitment Committee. BE.d Marks added as per dcuments provided, But physical education can't be added because they are not relavent .	—



27	04-Nov-16	Mir Alam Shahwani	Quetta 0333-7812784	Complaint was recorded regarding NTS result. Ms.Rahila Rahim had her B. Ed degree with her and is not short listed.	05-11-16	Yes	DRC considered her request but she is on 85th number in merit	PTC Percentage has been given instead of B.Ed according to policy. And she is on 85th in merit list.
28	04-Nov-16	Khair un Nisa	Qila Saifulla UC Sadar Muslimbagh	Rectification of merit list (The Qualification marks were not included in merit list)	01-12-16	Yes	Marks got added in merit, Rectified by District Recruitment Committee	—
29	04-Nov-16	Sardar Bibi & Dowlat Bibi	Qila Saifulla UC Bandad Mirzai	Complain was stated regarding rectification of UC	01-12-16	Yes	Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee	—
30	05-Nov-16	Gul Sumaira D/o Qalandar Khan	Zhob UC Meena Bazar	Objection on not including B.A marks in NTS merit result.	24-12-16	Yes	Issue resolved by District Recruitment Committee . Marks added as per documents provided.	—
31	11-Nov-16	Razia Gul D/o Haji Muhammad Syed	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated regarding rectification of UC	02-12-16	Yes	Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee	—
32	11-Nov-16	Froza Khanum	UC Narezai	Complain application was regarding NTS merit list	24-12-16	Yes	Candidate were informed about final merit as per NTS result and District Recruitment Committee working. issue resolved by District Recruitment Committee	—
33	2nd Dec - 2016	Muhammad Rafique	Musa Khail 0335-7418858	Complaint was submitted on subject of school selection. He claimed that the selected school in his town is located on 50 meters only while the school they applied for is located on 2 km distance and the enrolment of students too is more than the selected school .	27th Dec-2016	Yes	On this complaint, PMU has formed a committee of SMIP team and sent to re-visit the selected site (Killi Dargai hassankhail) and committee reported that there is no government school at the distance of 02 Km from the site. A report with GPS coordinates has been verified by SMIP team.	—
34	26th Dec - 2016	Abdul Sattar	Zhob 0313-8820907	Complaint application was submitted regarding Final Merit list of NTS test for JVT, his candidate Ms. Ameer Bakhta was 3rd in the list though she had her PTC degree with her and the candidate who was at the 2nd number had no PTC degree but that candidate had higher marks in NTS.	26th Dec-2016	Yes	His case was dealt by Naseebullah ( M&E Manager), Jahanzeb Nasar( Legal Officer) and Kulsoom ( Program Associate). The team listened to his complain and was explained the recruitment policy in detail , the complainant was satisfied then.	—
35	28th Dec - 2016	Abdul Aziz	Washuk 0336-3959675	Submission of letter ( Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list.	2nd Jan-2016	Yes	The case has been resolved the land mutated	Resolved.

36	30th Dec - 2016	Khaliqdad	Muslim Bagh 0335-2700714	In advertisement the U.C for which candidate Ms.Khair un Nisa was shortlisted was Sultan Zai but actually the school is situated in Sara Gharh U.C, so Mr.Khaliqdad came to discuss the case with concern officer, for officer was not available so Naseebullah ( M&E Manager) dealt.	21st Feb, 2017	Yes	Babar Jaffar ( E.O) dealt the case and complainant was told that letter is sent to DC for verification of UC , as soon as UC is verified he shall be informed by BEP team. After Final merit got signed, DRC received several complaints against merit regarding UCs issue. This issue is highlighted under DRC which is being addressed. The revised final merit will be signed in coming week.	—
37	12-Mar -17	Tayyeba Rassheed 5310342662 581	Kachhi Bolan	The complaint was received via e.mail . There was mentioned that the candidat Ms.Tayyeba Rasheed had applied for the post of JVT for a school in 2013 but she was not selected and there were 3 posts vacant and only one candidate was selected . As two posts are vacant so BEP should assign the vacant post to the above mentioned candidate.	13th March 2017.	Yes	The complain was discussed with Abdul Qayyum (Program Assistant) called the candidate and talked to her husband and told the complainant that this case belongs to PGEB project which is afterwards handed over to Government, so the Complainant should submit his request to Education Department but he(The candidate's husband) was rudely denying the fact and said that if your project will not facilitate us then i will go to world bank against you people.	Resolved.
38	15-Mar -17	Muhammad Naveed	Barkhan 0333-7736238	The complain was received via text on our official contact number, there was stated that the applicant Muhammad Naveed has appeared in test for ( MonitoringAssociate) in RTSM PMC on 20th Nov-2016 and he also appeared in interview on 13th Dec-2016 but still has no clue about final selection.	15-Mar-17	Yes	The complain was discussed with Ahsan Jamil ( HR officer) , the candidate is on waiting list said HR Officer.	Resolved.
39	17-Mar -17	Sorab Khan 55202-146312-5	Kohlu 0331-8031145	The complainant visited BEP head office and recorded his complain to Mr.Naseebullah (M&E Manager), the complain gist was regarding school selection in Kohlu district, the school application form was submitted on 25th Feb-2016 and applicant name was Jamal Khan ( village : Kili Darwaish abad Tamboo) but his application was not shotlisted and the BEP team selected a nearby town while both the application was submitted on same date.	17-Mar-17	Yes	The case was dealt by Naseebullah ( M&E Manager) and Latif Marri (E.O) , they explained to him that the other application was selected for there are more enrollement of students than that of his recommended town, google map was shown to him and the BEP team made him convinced that the students of his town can also go to the selected school easily.	Resolved.
40	20th-Mar ch-2017	Saleh Muhammad District Member Nakas 2	Hernai	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliar pedri and killi raza muhammad. He claimed that these Schools belong to unin council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrag.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.

41	20th-Mar-2017	Muhammad Ramzan S/o Amir Muhammad	Hernai, UC Nakas2	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliar pedri and killi raza muhammad. He claimed that these Schools belong to Union Council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrag. Further more two candidates Miss Nahida Tareen and Miss Sumayya Tareen are of other UC but these candidate names have been included in Nakas 2 U.C.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
42	20th-Mar-2017	Esmatullah S/o Nasrullah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliar Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
43	20th-Mar-2017	Muhammad Salim S/o Haji Muhammad Siddique	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliar Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
44	20th-Mar-2018	Khair Shah S/o Syed Nadir Shah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliar Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
45	27-Mar-17	Sultana D/o Rakhal Shah	Qalat	Guidance required teacher recruitment under BEP, Community members Khadi Bangalzai has submitted Complain against Bibi Samina D/o Jalal Khan. She has changed her local certificate from Municipal Corporation to Union Council of Kalat.	District Recruitment Committee will take decision	Yes	action taken against complain and she has recommended against vacant post, approval has also taken by secretary education.	—

46	3rd-Apl-17	Naeem Shah S/o Haji Abdul Kareem 54400-0509307-3	Ziyarat Sanjavi 0345-8326567	In his application it was stated that his candidates who actually belong to U.C 'Poi' but in NTS result which was held on 24th Jan-2017 the candidates are included in UC "Kach", He wants their names to be listed for U.C "Poi" where they really belong from.	Case is forwarded to DRC	Yes	Case was addressed to DRC by Education Officer Babar Jaffar. And DRC listed their names for U.C Poi.	—
47	18th April-2017	Duniya Khan S/O Shinee Gul 56201-1770383-9	Muhammad Rafique, Alghouri Boot House, Wasey Market Killa Saifullah	it is stated in the received document that the village kiili Touda Ghazgai Ghorezai killa saifullah is selected for establishing a school as per the need of the area. As the natives are ready to facilitate Balochistan Education Project by providing Female candidates and any kind of support so it is requested to the Project Director to please do not cancel the school for the sake of the Education and future of the local kids.	16-05-17	Yes	Annanounced NTS for 3 times, but teacher didn't found in the UC. Other UC /tehsil Teacher can't perform there duties as the area is flung from city. As per discussion with Manger Education, the site is temporarily dropped. Will go for male option, if having less than target schools in district.	Resolved.
48	12th April-2017	abdul Qadir S/O Allah Dinah 53302-2090922-9	Abdul Qadir S/O Allah Dinah, Nafoorullah Dinah, Majeedana Magsi, Tehsil and District Jhal Magsi.	The Complainant says that I have donated land for the establishment of Schools to Government of Balochistan Secondary Education Department after the selection of site and as promised by the representatives of BEP one post was to be nominated from my family in return to the land and rooms i gave to government but BEP did not recruit my candidate after NTS Test.	12th April-2017	Yes	—	District Recruitment Committee rejected the complaint because it is not in recruitment policy and no hiring has taken place yet in said village.
49	19th April-2017	did not provide his personal information due to Tribal Affairs at their village. Only phone No. is provided i.e. 0333793564 7, UC LOTI, District Dera Bugti.	333793564 7	There were three applicants who had submitted the grievance that instead of their deserving sites namely ; 1. Killi Dr Saifuddin Shambani, 2. Killi Noor Muhammad Shambani, and 3. Kiili Pehelwan Shambani another three sites were selected for schools i.e. 1. Killi kehlani UC Loti, 2. Goor Shamool UC Loti, and 3. Phogani UC Loti. They have appealed for Justice to Worthy Project Director.	25-April-2017	Yes	—	The applicant was contacted to provide justification to the decision taken by PMU regarding school selection criteria however the applicant did not respond. It must be noted that the District wise target of Dera Bugti was 23 and the sites were finalized on the basis of Enrolment, Distance from next level and security where construction could be executed. The said Union Council is one of the disturbed areas where project activities may not be possible to conduct.

50	17th-04-2017	Sania Jalal D/o Mir Jalal Khan 51202-1521900-6	U.C Pandran, Tehsil Kalat, Kalat.	Complain was received via TCS. She is on 2nd No. in UC and affidavit of being Rejected as candidate on third no. in Union Council Miss Bibi Sultana has submitted complain against her for changing her UC from MC Kalat to Pandran.	Case is already in DRC	Yes	case is rejected by DRC	The local certificate was made after due date of advertisement.
----	--------------	--	---	--	------------------------	-----	-------------------------	---

Court Cases (Mohtasib, Honourable High Court and Honourable Supreme Court)

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	08-Nov-16	Mashoor Bibi	Jaffarabad	Complain was submitted regarding teacher recruitment.( Case against PGEB recruitment process)	Hearings to be fixed by the Hon'ble Supreme Court of Pakistan	Case Subjudised before the Hon'ble Supreme Court of Pakistan	Case pertains to PGEB project and review application is under trial in Honourable Supreme Court of Pakistan. Mr. Haroon DS (Judicial) Education Department has attended court on behalf of Education Department and project in Islamabad on 17-11-2016.	Pending
2	8th Dec -16	Zahidullah Khan s/o Zarif Khan VS SHO Police Station Hub and others	Lasbella Gulshan Colony Tehsil Hub	A Complaint was recorded before the Hon'ble High Court of Balochistan that the land gifted and dedicated for school which was supposed to be built by PGEB has been confiscated. Therefore, the Hon'ble Court through Order Dated 8.12.2016 in a case called Zahidullah Khan VS SHO Hub and others (Criminal Miscellaneous Quashment No 111 of 2013), deputed the Legal officer of GPE to visit the site and take over the possession of the said land with the help of SHO, Police Station Hub, and the Revenue staff.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 07 December 2018	yes	The land has been officially transferred in the name of "Secondary Education Department, Government of Balochistan". The details of the area of the land as well as the exact location of the land has been recorded on the mutation (Fard) document. The Revenue Record in the office of Tehseel, at Tehsil Hub, District Lasbella has been updated to this effect and the mutation document has been acquired. A new primary school is being proposed under BEP project	Case Resolved

3	20-Dec-16	MS. Shahina /Do Noor ur Haq	Qila Saifullah	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining second position in entry test, she still was not considered for the job by PGEB authorities.	The case has been argued before the Hon'ble Ombudsman (Mohtasib) Secretariate Balochistan, Quetta, and is awaiting for the Judgment to be announced by the Hon'ble Secretariate	Judgment Pending	Mr. Jahanzaib Nasir legal Officer argued the case before the Hon'ble Ombudsman, Balochistan, and the written Judgment is awaited	Pending
4	22nd Feb - 2017	Wadera Nihal Khan	Dera Bogti	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection.	Two written replies from the GPE-BEP have been submitted on 11th May 2017 as well as on 07th March 2017, and the disposal of the matter is still pending.	Disposed of as being withdrawn by the Complainant. Whereas, the official finding from the Hon'ble Ombudsman still awaited	The Formal intimation of the withdrawal of the Complainant is still awaited	Disposed off
5	22nd Feb - 2017	Bashiran Bibi	Jaffarabad	Petition submitted before Honorable Supreme Court of Pakistan, regarding teacher recruitment,	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble Supreme Court of Pakistan.	Pending
6	20-Mar-17	Akhtar Shah Mandokhail	Zhob	complaint submitted before the Hon'ble Ombudsman, Balochistan, Quetta. The Complain complaint pertains to be against the recruitment of the Teaching staff. The copy of the complaint and the Notice from the Hon'ble Ombudsman Secretariate has been received recently (19th July-2017) and the Legal Officer has appeared before the Authority and waved off the notice. the reply to the complaint along with the relevant supporting documents will be submitted in due course.	NA	Judgment Pending	Pending	—

7	28th Mar - 2017	Haji Muhammad Azeem Khan and Sons	Qilla Saifullah	Legal Notice from "Mr Iqbal Ahmad Kasi Advocate Law Firm", on behalf of Haji Mohammad Azeem Khan and Sons was received in dispute over Procurement for different packages including construction /Rehabilitation of schools (12 Primary and 1 Middle) in Balochistan.	10th Apl- 2017	Yes	The Legal Notice has been replied in writing, and sent the reply through TCS Courier on Dated 10th April 2017 and the matter had then been settled and resolved.	Resolved.
8	5th Apl- 2017	Sahib Zadi D/o Mir Khan	Barkhan	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as EST.	A written reply from the GPE-BEP has been submitted on 30th March 2018 and the matter was disposed of mainly on the grounds argued in the same reply	Complaint is Dismissed on 15th August 2018, pursuant to the Letter bearing Number 168/2018/PMS/01024523, Dated 20 August 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	Complaint is Dismissed on the grounds that the Complainant did not fulfill the criteria of becoming as an "EST" teacher as per policy laid by the Education Department.	Disposed off.

9	23rd Apr-2017	Sehrish David D/o Jhon David	Nawa Killi Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding JET teacher against Daughter Quota...	the complain t, after being prproperl y written replied by GPE-BEP on 06th April 2018, has been disposed off by the Hon'ble Ombuds man on the terms that the Applica nt has to approac h the proper forum	Complain t is Diispose d of on 11th april 2018, pursuant to the Letter bearing Number 720/2018/PMS/5 10-12, Dated 13 April 2018. The Complain ant has been referred to present their case before the Secretar y Educatio n who would e in a better position to address the matter. The Judgmen t of the Hon'ble Ombuds man received and has been placed in Record	Complaint is Dismissed on the grounds that the Complainant has to approach a proper forum.	Disposed off
10	21-Jun-17	Bibi Rehana	Ziyarat	Constitutional Petition No 653 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 21st June 2017 by the two Petitioners namely Bibi Rehana and Bibi Rakia against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner and the District Education Officer of the Ziarat District, whereas, the Notice from the Hon,ble Court has been received recently on 17 july 2017. The matter pertains to be against the recruitmrnt of the female teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice.	NA	Judgmen t Pending	Pending	—



11	08-Jul-17	Nasrullah S/o Allahdad	Musakhail	Notice has been received from Hon'ble High Court of Balochistan from Nasrullah Son Of Allah Dad, gist of grievance is not mentioned as yet, hearing is on 217th December 018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 17 December 2018	Pending	Pending	Pending
12	17-Aug-17	Tahira Bibi D/o Allah Dina	Jhal Magsi	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP have been submitted on 24th August 2017 and the matter was disposed of mainly on the grounds argued in the same reply	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at her case on merit. The official finding from the Hon'ble Ombudsman has been received pursuant to the Letter bearing Number 293/2017/PMS/Jhal Magsi/755-56, Dated 08 November 2017	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at her case on merit	Disposed off.
13	21st Aug - 2017	Samad Khan Saqi S/o Ab.Hameed	Samad Khan Saqi and Brothers Zhob Ph:031121 21812 Mob:0320 8860393	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 15 Middle) District Sherani of Package/Activity No 50	Two written replies from the GPE-BEP have been submitted on 27th September 2017 as well as 19th March 2018, and the disposal of the	Judgment Pending	Pending	

					matter is still pending.			
14	21st Aug - 2017	Abdul Qayyum S/o Haji Habibullah	Afghan construction company Zhob Mob:0341 2882884	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid for procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 12 Middle) District Zhob, Qamardin of Package/Activity No 48	A thorough written reply from the GPE-BEP has been submitted on 27th September 2017, and the matter was disposed of mainly on the grounds argued in the same reply	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at their case on merit. The official finding from the Hon'ble Ombudsman has been received pursuant to the Letter bearing Number 399/2017/PMS/Zhob/493-94, Dated 026 February 2018. The official finding from the Hon'ble Ombudsman has been received and has been kept as record	The Complaint was submitted on 01 August 2017, and the written reply was submitted by the GPE-BEP on 27 September 2017	Disposed off

15	26th Sep - 2017	Hajira D/o Karim Baksh	Kech	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining 1st position in entry test, she still was not considered for the job by DRC.	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman on the terms that the Applicant has to approach the proper forum	Complaint is Dismissed on 15th August 2018, pursuant to the Letter bearing Number 168/2018/PMS/1024-25, Dated 20 August 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	The Complaint has been disposed off (Dismissed) by the Hon'ble Ombudsman on the terms that the Applicant has no Associate Degree in Education (ADE), hence the same was dismissed	Disposed off
16	09th Oct- 2017	Saima D/o Nasir	Khuzdar	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Khuzdar Balochistan, there was filed a complain with the averment that the recruitment committee of DRC Sikanda abad Tehsil Sorab objection on merit list and pointed out that non inclusion of name in merit list and appointed another candidate who belongs to another district.	Pending	Yes	the complaint has been received on 09th October 2017 and since then has not been pressed any further	Pending
17	13-Oct- 17	Saadiqa Bibi D/o Niamatullah	Muslim Bagh	A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment that the candidate is the resident of the village (Zharhi Muslim Bagh) and has passed NTS test despite that candidates from other far situated villages are hired for the posts advertised.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 30th May 2018. On 24th of October 2018, the final arguments have been given before the Bench	Pending	Pending	Pending

					headed by the Hon'ble Chief Justice of Balochistan. Whereas, the case has been reserved for final Order to be announced soon.			
18	26th Oct-2017	Zar Khatoon	—	Notice has been received from Hon'ble High Court of Balochistan from Zar Khatoon, gist of grievance is not mentioned as yet, hearing is on 21st Aug-2018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 1st November 2018	Pending	Pending	Pending
19	26th Oct-2017	Bibi Rehana D/o Shah Buzerg Rakkia D/o Abdul Sattar	Ziyarat	A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment, the petitioners claim that the abundant building in Killi Zargai UC Spezandi Tehsil district Ziyarat which is going to be functional via BEP so new vacancies must be created for the said school.	19th Oct-2017	Yes	the Petition was disposed off Dated 19 October 2017, on the terms that the School will be handed back over to the GPE-BEP, who then will functionalise the school and hand over the appointment letters to the two Petitioners	Disopossed off
20	1st Nov - 2017	Shah Gul S/o Shadi Gul	Musa Khail	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection.	Two thorough written replies from the GPE-BEP have been submitted on 24th August 2017 as well as on 12 February 2018, and the disposal of the	Pending	Pending	Pending

					matter is still pending.			
21	21st Nov - 2017	Kaleemullah	Sun rise solar system Company.	Legal Notice from "Niamatullah Batezai Law Firm", on behalf of Mr Kaleemullah was received in a dispute over Procurement for scheme of 10 KV solar system for schools in Balochistan.	—	Yes	The same Legal Notice has been replied in detailed and comprehensive manner in writing and posted on through TCS Courier on Dated 21st November 2017	Replied
22	26th Dec - 2017	Rabia Kakar D/o Abdul Hameed	Loralai	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Loralai Balochistan, regarding JVT teacher recruitment.	Pending	Yes	Two written replies Dated 09th January 2018 submitted in person as well as reply Dated 06th April 2018 despatched through Courier has been submitted and the outcome is still awaited	Pending
23	8th Jan- 2018	Saeeda Noor D/o Haji Noor Ahmed	Noshki	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	Pending	Yes	Fresh Petition and the reply is still awaiting, still pending before the Hon'ble Ombudsman	Pending
24	8th Jan- 2018	Samaira Naz	Panjgur	Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,.	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench.	Pending
25	11th Jan- 2018	Taj Muammah Naik Muhammad Ghul Rasool Sons of Ali Jan	Sibi	the Plaintiff was initially filed before the Civil Judge Mach, wherein, the stay Application of the Plaintiff against the building of the school was dismissed after a written reply submitted by the GPE-BEP. Further, the Plaintiff then preferred an Appeal against the Order of the Civil Judge before the District and session judge (Sibi).	Pending	Yes	the matter is still pending.	Pending

26	17th Jan-2018	Ayesha D/o Dostain	Dera Bogti	Complain was submitted before the District and session judge (Sibi) , regarding teacher recruitment.	–	Yes	The Petition has been disposed off on Dated 27th December 2017, in a terms that the matter has to be taken and decided by the District Rederessal Committee (DRC)	Disposed off.
27	15-Jan-18	Bibi Saleema D/O Haji Abdul Rehman	Qilla Abdullah	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment as "JVT".	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman as the Contract of the Complainant was already been awarded to the Complainant	Complaint is Disposed of on 07th August 2018, pursuant to the Letter bearing Number 15/2018 /PMS/10 05-1009, Dated 15th August 2018. The query of the Complainant was resolved	The query of the Complainant was resolved and the Judgment of the Hon'ble Ombudsman received and has been placed in Record	Disposed off
28	1st Mar - 2018	Sher Jan S/o Marjan	Zhob	Appeal was submitted before the District and session judge (Zhob) , dispute was over the school site selection.	–	Yes	the matter was resolved between the parties on the terms that the school building will built over the same site selected by the GPE-BEP, through proper site selection mechanism, and the troubling parties were restrained from interfering into the process of building the school.	Resolved.
29	20th Mar - 2018	Asma Hussain D/o Nisar Hussain	Sariyab road Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as J.V teacher..	Pending	Yes	A written reply from the GPE-BEP has been submitted on 20th March 2018, and the disposal of the matter is still pending	Pending
30	29th Mar - 2018	Jamila Usman	Panjgur	Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,.	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench.	Pending

31	08th March 2018	Ms Rani Kakar D/O Ali Mohammad	Sinjavi, Ziarat	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A thorough written reply from the GPE-BEP has been submitted on 16th May 2018, and the matter was disposed of mainly on the grounds argued in the same reply	Complaint was found to be frivolous and without merit, hence dismissed by the Hon'ble Ombudsman, Balochistan. Complaint is Dismissed on 15th September 2018, pursuant to the Letter bearing Number 195/2018/PMS/123,-24 Dated 26th September 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	The Complainant was not found to be the competent candidate to teach the children and pursue a career as a teacher	Disposed off
32	6th April 2018	Amina Bibi D/o Bismillah	Dera Allahyar	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Naseerabad at DM Jmaali Balochistan, regarding teacher recruitment.	Pending	Yes	Written Reply of the Complaint has been despatched through TCS Courier Dated 06th April 2018, and the outcome of the matter is awaited	Pending

33	11-Apr-18	Saleeqa sayyad W/O Rafeeullah	Loralai	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment appointment as E. S. T..	A written reply along with its Annexures from the GPE-BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman mainly on the grounds argued in the same reply	Complaint is Disposed of on 15th August 2018, pursuant to the Letter bearing Number 532/2018/PMS/1020-21, Dated 20th August 2018. The Complaint was dismissed on the grounds that the Complainant had no requisite Associate Degree in Education (ADE) for the post of E.S.T.	The Complaint has been disposed off (Dismissed) by the Hon'ble Ombudsman on the terms that the Applicant has no Associate Degree in Education (ADE), hence the same was dismissed	Disposed off
34	22-Jun-18	Sadiqa Bibi D/o Abdul Salam	—	Notice has been received from Hon'ble High Court of Balochistan from Sadiqa Bibi, gist of grievance is not mentioned as yet, hearing is on 21st November 018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 21st November 2018	Yes	—	Pending
35	22-Jun-18	Kiran Khalid	Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the disposal of the matter is still pending	Pending	Pending	Pending



36	08-Jun-18	Masooda razaq	Baghbana, Khuzdar	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP has been submitted on 31st July 2018 and the matter was disposed of in directing the Respondents to appoint the Applicant	Complainant is Disposed of on 04th September 2018, pursuant to the Letter bearing Number 346/2017/PMS/1083-85, Dated 11th September 2018. The Respondents have been directed to appoint the Complainant after completion of all codal formalities to become a JVT	Complaint is allowed and the Judgment of the Hon'ble Ombudsman received and has been placed in Record	Disposed off
----	-----------	---------------	-------------------	--	--	---	---	--------------

### Procurement Grievances

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	04-Feb-16	Israr Panezai (CEO) Shaor Org	Quetta 0300-9387204	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. Despite several attempts, the required information on firms behalf, as a result they did not meet eligibility criteria of qualification and thus they were considered as non-responsive.	24-02-16	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, SHAOR was found to be responsive as per the technical requirements and further allowed to participate in the financial opening.	The grievance is addressed

2	19-Feb-16	Nadir Gul Barhech (CEO) BRSP	Quetta 0812-471437-9	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, BRSP was found to be responsive as per the technical requirements and further allowed to participate in the financial opening.	The grievance is addressed
3	16-Feb-16	Ahmed Khan Kakar (AM) JV MDF and GRHO	Quetta 0333-7846660	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re-evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ), Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
4	22-Feb-16	Ihtram Majid (CEO) BRDRS	Quetta 0333-7818478	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ), Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). BRDRS was found to be responsive as per the technical requirements and further involved in the financial opening.	The grievance is addressed.
5	23-Feb-16	Hameedullah Kakar Youth Org	Quetta 0346-8397898	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ), Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
