

*QUARTERLY PROGRESS REPORT*

**GLOBAL PARTNERSHIP FOR EDUCATION-BALUCHISTAN EDUCATION PROJECT**

**SECONDARY EDUCATION DEPARTMENT**

**GOVERNMENT OF BALUCHISTAN**



*For the Quarter*

*Oct – Dec 2018*

**Project ID- P144454**

**Prepared by Manager M&E GPE/BEP**

**Executive Summary:** Project Management Unit (PMU), Global Partnership for Education-Balochistan Education Project (GPE-BEP) is implementing a three year project under the supervision of World Bank. The PMU has identified and notified all 725 locations for new primary schools and all 95 primary schools to middle and 25 middle schools to high level for up-gradation with set notified criteria. 1534 teachers have been recruited and deployed for 790 newly established and 120 upgradation schools. Recruitment of all the target teachers under the project is complete.

Per BEP MIS Dashboard, 1796 (90%) total teachers have been trained against the target of 1988 under the project. The teachers trained include the ECE teachers, EST teachers, and Head teachers of the project schools.

In the reporting period, K-5 students' total enrollment has been reported as 56308 in 670 new established primary schools, and 120 (95 Middle and 25 High) established up-gradation schools. This enrolment achieves 133% of project total enrolment target (42308) of K-5. The enrollment segregated gender wise makes it 38366 of girls enrollment and 17942 of girls enrollment in grade K-5 in the project supported schools.

The retention of the students in the project schools has been calculated before last quarter .i.e. Jan-Mar, 2018. The students' retention is calculated as 81% against the project target of 75% for the project year two. The retention is calculated of 303 schools which have completed their one year study session and started the second year. The target is achieved at commendable ratio of 108%. The calculation of retention for third year is due in coming quarter. However, it will be challenging to report if SMIPs are not on board with PMU.

Furthermore, 829 total schools were advertised for construction works. Contracts have been awarded to start works in 811 schools. 709 schools have completed their construction works whereas 102 schools' works are under final stages and complete their works by coming quarter.

Early Childhood Education-ECE kits were procured for 840 schools, in addition Taleemi Basta for ECE and Multi-grade classes was procured for all 845 schools. In the reporting period, ECE Program has been established in 808 schools including 688 newly established schools and 120 upgraded schools and 790 schools have been provided with the TLM kits. Simultaneously, 743 schools have been provided with the furniture including blackboard.

# Contents


<b>Results based progress .....</b>	<b>4</b>
<b>1. Project Development Objective .....</b>	<b>4</b>
<b>1.1 Girls enrolled in grades K-5 of project supported government schools .....</b>	<b>4</b>
<b>1.2 Boys enrolled in grades K-5 of project supported government schools.....</b>	<b>4</b>
<b>1.3. Girls enrolled in grades 6-10 of project supported government schools.....</b>	<b>5</b>
<b>2.0. Intermediate Results.....</b>	<b>6</b>
<b>2.1. Number of new primary schools established through community support .....</b>	<b>6</b>
<b>2.2. Number of schools upgraded from primary to middle level .....</b>	<b>6</b>
<b>2.3. Number of schools upgraded from middle to high/higher secondary level.....</b>	<b>7</b>
<b>2.0.1. Development Progress by Reporting Qtr</b>	
<b>2.4. Number of government schools to which furniture (incl blackboard) is provided</b>	
<b>2.5. Number of schools to which TLM kits provided .....</b>	<b>8</b>
<b>2.6. Number of government schools in which ECE program established .....</b>	<b>8</b>
<b>2.7. Number of PTSMC members trained in targeted project schools .....</b>	<b>9</b>
<b>2.8. Number of teaching staff trained in the project specific schools .....</b>	<b>9</b>
<b>3.0. Detail table of the set target achievement against the result framework .....</b>	<b>9</b>
<b>4.0. Grievance Redressal Mechanism (GRM):.....</b>	<b>10</b>

# Results based progress

## 1. Project Development Objectives

### 1.1 Girls enrolled in grades K-5 of project supported government schools


- **Progress:** The enrollment of 38366 in the bar chart is the result of the restless effort of all the PMU program sections. The enrolment/schools increased from 37400/755 of the previous quarter to 38366/790 in the reporting period at ratio from 139% to 143% of the total project enrolment target. The 790 schools given in the bar include the enrolment of 670 newly established and 120 up-gradation schools for the reporting period. The K-5 girls enrolment has been achieved over 100%.

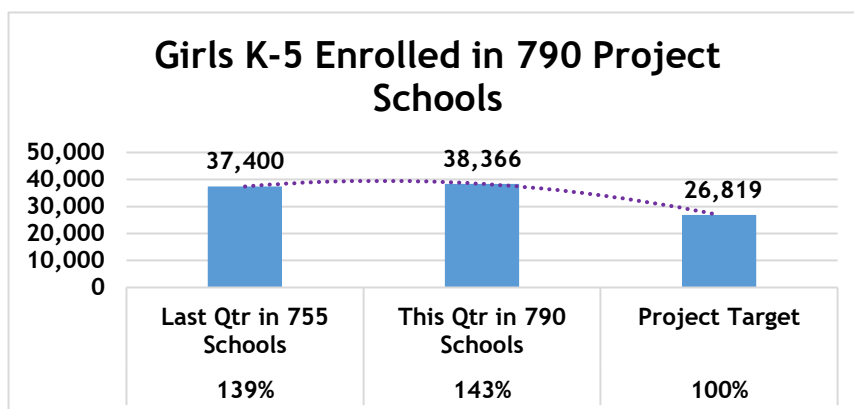

- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.
- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools.
- **Challenge(s):** It is expected that PMU does not have SMIPs on board after the end of BEP project. It may be challenging for the Education Department regular monitoring mechanism to retain this enrollment. However, PMU will hold a meeting with PMC Program Manager to look after the enrollment of these schools with the help of RTSM teams in the field.

### 1.2 Boys enrolled in grades K-5 of project supported government schools

- **Progress:** The enrollment of 17942 in the bar chart is the result of the restless effort of all the PMU program sections. The enrolment/schools increased from 16933/755 of the previous quarter to 17942/790 in the reporting period at ratio from 109% to 116% of the total project enrolment target. The 790 schools given in the bar include the enrolment of 670 newly established and 120 up-gradation schools for the reporting period. The K-5 girls enrolment has been achieved over 100%.

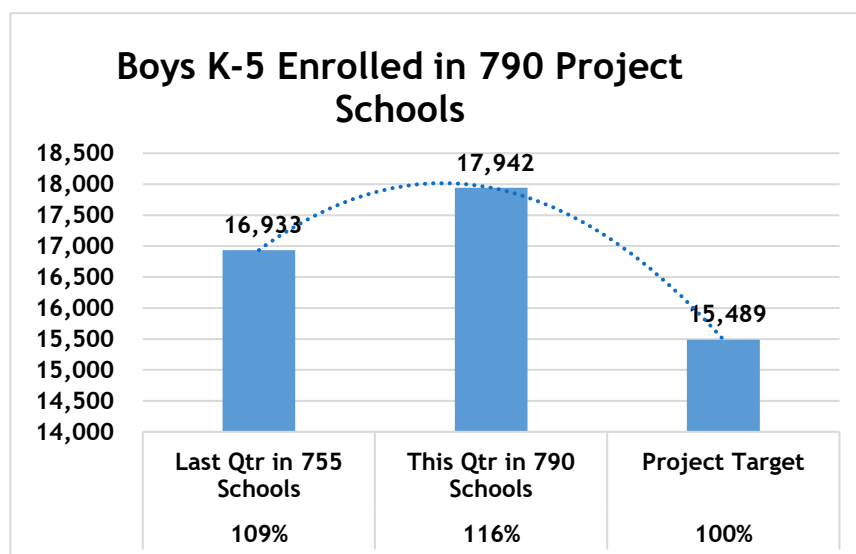


- **Lesson(s) learned:** While selecting the schools, maximum enrollment-potential locations should be selected.
- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools.

- **Challenges:** It is expected that PMU does not have SMIPs on board after the end of BEP project. It may be challenging for the Education Department regular monitoring mechanism to retain this enrollment. However, PMU will hold a meeting with PMC Program Manager to look after the enrollment of these schools with the help of RTSM teams in the field.

### 1.3. Girls enrolled in grades 6-10 of project supported government schools


- **Progress:** The enrollment of 6-10 girls in the reporting quarter is 3127 in 120 schools which is 170% of the set target. This project indicator has been achieved over 100%. The enrollment of girls 6-10 is achieved from project supported upgradation schools. However, the construction works completion, provision of material and teachers arranged for upgraded schools have highly encouraged the enrollment in these schools. The upgraded schools have entirely been selected on available higher enrolment and higher potential enrolment for the upgraded levels.

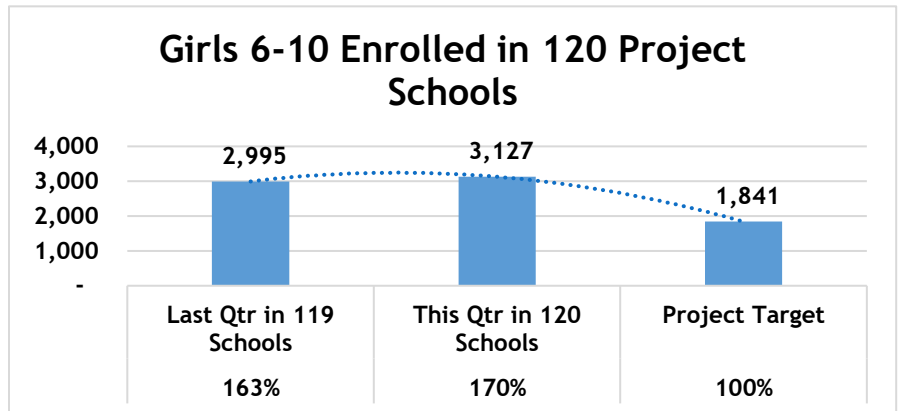

- **Lesson(s) learned:** The schools with high enrolment and feeder schools should be selected for up-gradation.
- **Recommendation(s):** The Education Officers should randomly validate the enrollment of at least 25% reported schools. The enrolment should be validated and mobilized to be retained at schools.
- **Challenges:** It is expected that PMU does not have SMIPs on board after the end of BEP project. It may be challenging for the Education Department regular monitoring mechanism to retain this enrollment. However, PMU will hold a meeting with PMC Program Manager to look after the enrollment of these schools with the help of RTSM teams in the field.

### 1.4. Students retention in project schools

**-Progress:** The students retention in 303 schools has been calculated as 81% against the 75% target for the year two in previous quarter which determines the response value of the community towards the design and operations of the schools and hard work of the field staff over the mobilization of community to retain the students at the schools. It is very encouraging to see that the target is achieved at the rate of 108%. The target has been calculated for project year two though these 303 schools have completed their year one of the study session. The retention has been calculated with the formula as follows:

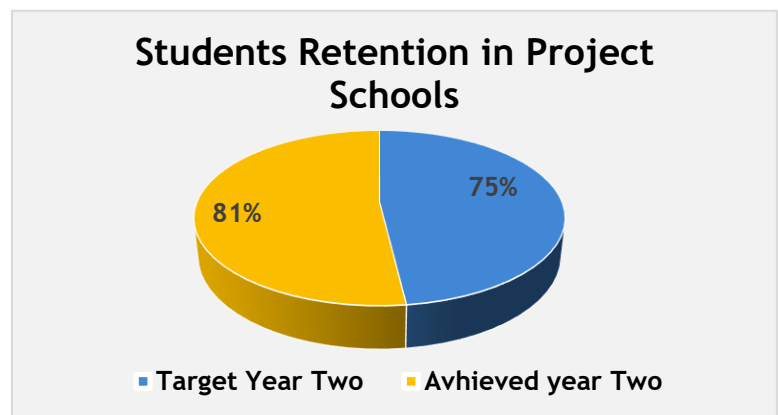


$$\frac{\text{Y2 total enrollment} - \text{Y2 total new enrollment}}{\text{Y1 total enrollment}} \times 100 = \text{Retention}$$

- **Lesson(s) learned:** Regular monitoring and follow up of the students attendance at the schools resulted this encouraging achievement.

## 2.0. Intermediate Results

### 2.1. Number of new primary schools established through community support

- **Progress:** The chart shows that 670 of 725 schools have been established. The chart shows that the schools establishment ratio has comparatively been improved from last quarter as 88% and this reporting period as 92%. Education section has reported that 21 of new primary schools will not be opened due to various security and feasibility reasons. 1308 JVT teachers have been hired for these primary schools and the due number has been deployed in 670 newly established primary schools. 34 of the schools have been reported 'closed' due to teachers absenteeism and non-joining issues. The number of hired teachers also includes the teachers for the temporarily closed 34 schools.

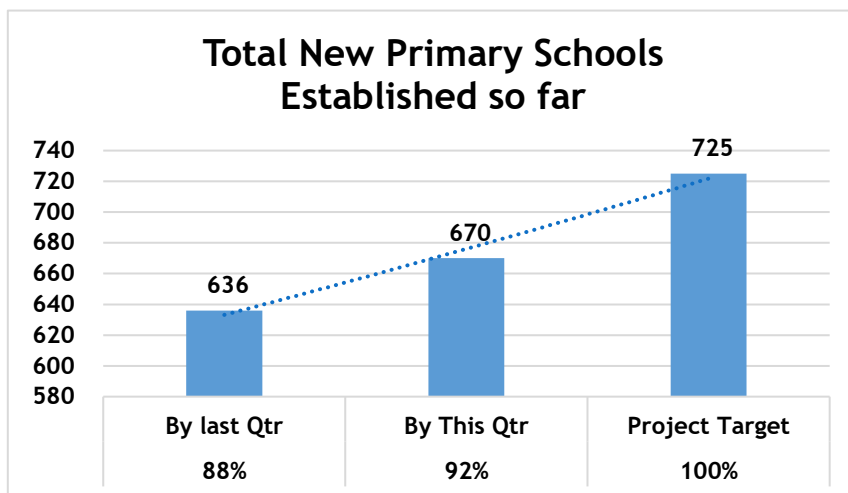


- **Lessons learned:** The PMU should ensure that all the concerned UCs villages' candidates have received the information in regard to applying for the concerned schools. Few of the concerned UCs candidates did not apply for the NTS tests. The teachers hiring process is cumbersome under the project.

**Recommendation(s):** Through all the available means, PMU must ensure that the concerned villages receive the information in regard to schools for applying NTS tests. The teachers hiring process may be reviewed for any upcoming project.

### 2.2. Number of schools upgraded from primary to middle level


**Activity Updates:** There is target of 95 middle schools upgradation from the Primary level in the project. All the 95 schools have been identified and notified. PMU started working on upgradation activities in 100% of the upgraded schools. Most of the activities have been completed. It is reported that 79 of 95 middle schools have started studied in class 6 or above with 1291 enrollment contributing into total middle level enrollment.

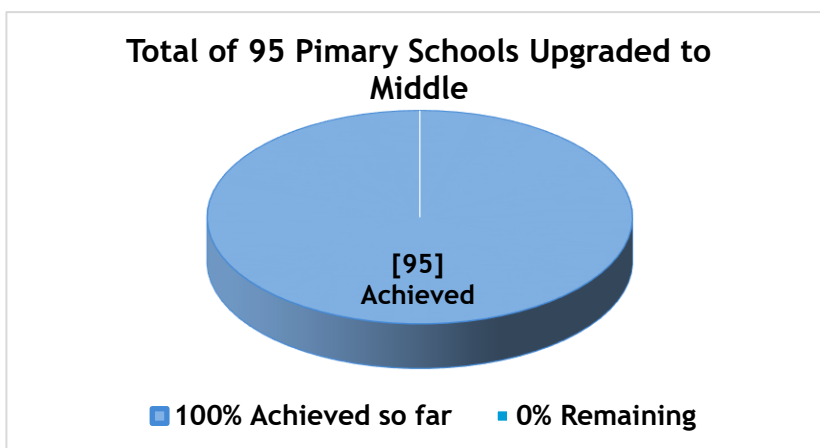

## 2.3. Number of schools upgraded from middle to high/higher secondary level

**Activity Updates:** There is target of 25 high schools upgradation from the Middle level in the project. All 25 schools have been identified and notified. PMU started working on upgradation activities in 100% of the upgraded schools. Most of the activities have been completed. It is reported that 14 of 25 High schools have started studied in class 9 or above with total enrollment of 449.

**Total of 25 Middle Schools Upgraded to High**

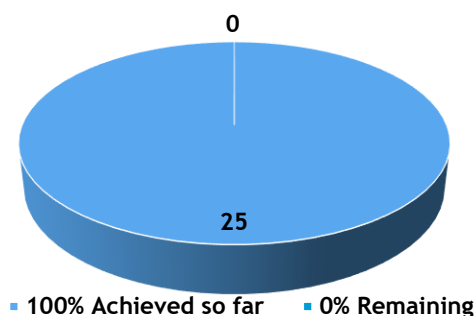

### 2.0.1. Development Works Progress by Reporting Quarter

Chart A


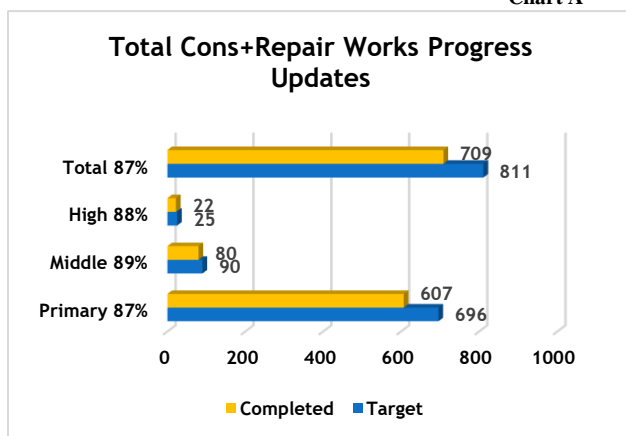


Chart B

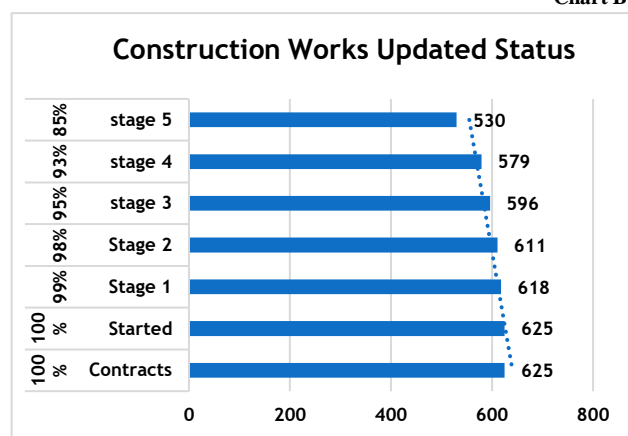


**Activity Updates:** The chart A gives updates of all the Schools works including full construction and repair works both. The chart A shows that 709 out of 811 total target schools have completed their stage 5 and repair works. This includes 607 primary schools, 80 middle schools and 22 high schools. The chart B shows construction progress of the schools with only construction works. The chart B shows that 530 of total 625 full construction target schools have completed stage 5 works. Whereas, 95 (15%) of the schools construction works are underway and most expectedly will complete the stage 5 works in the next reporting quarter.

Chart C

The chart C shows the progress of the schools only with the repair works. Total 179 (96%) of 186 schools are completed with the repair works which include 169 primary schools, 10 middle schools and 7 high schools.

**Total Repair Schools Progress Update Chart**

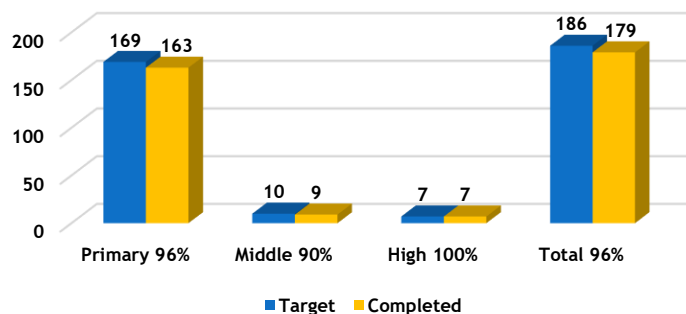




#### 2.4. Number of government schools to which furniture (incl blackboard) is provided

**Activity Updates:** The procurement of all the target schools have been made. PMU has provided 743 of 845 schools with the furniture including blackboard in the reporting period. However, it is expected that all the due schools will be reported completed as with provision of furniture including blackboard in the coming quarter.

**Total Schools Provided with Furniture Including Blackboard of 845 Total Target**

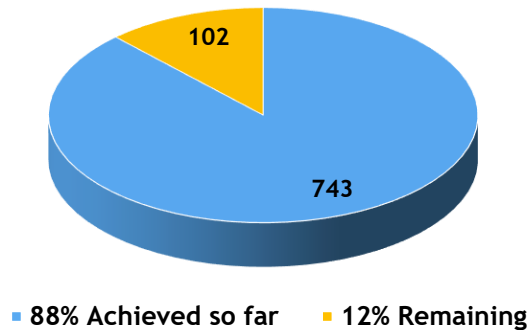


#### 2.5. Number of schools to which TLM kits provided

**Activity Updates:** All ECE TLM 365 Kits have been procured and distributed among 790 of 845 schools and will not be procured any further, the taaleemi basta and multi-grade bags have been procured for all the 845 schools.

The chart reports that PMU has provided 790 of 845 schools TLM kits so far. However, it is expected that all the due schools will be reported completed as with provision of TLM Kits in the coming quarter.


**Total Schools Provided with TLM Kits out of 845 Total Target**

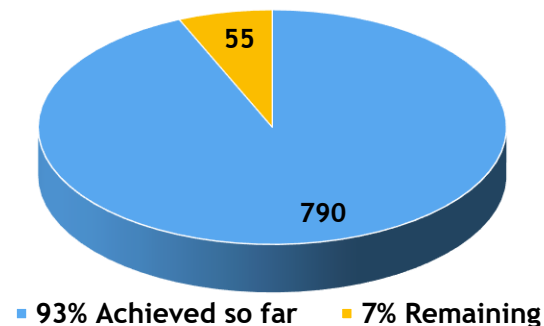

#### 2.6. Number of government schools in which ECE program established

**Activity Updates:** 808 of 845 schools are established with the ECE program under the project. The project target number is expected to be achieved in the coming quarter. Due to split items procurement and wide spread field, the ECE materials take time while supplying. However, the PMU expects that the remaining due schools supply and distribution will be completed by the coming quarter.


**Total of 845 Schools with ECE Program Established**

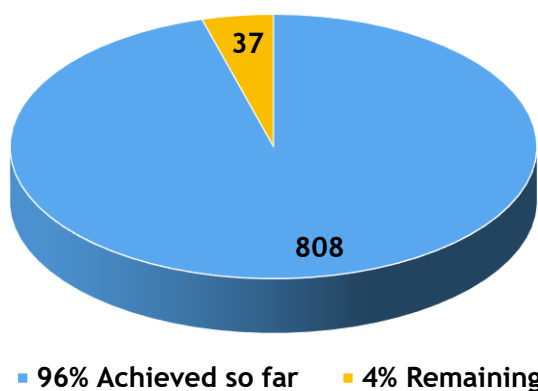



## 2.7. Number of PTSMC members trained in targeted project schools


**Activity Updates:** The chart shows that the number of 4160 of 4465 target PTSMC members has been trained by reporting quarter.

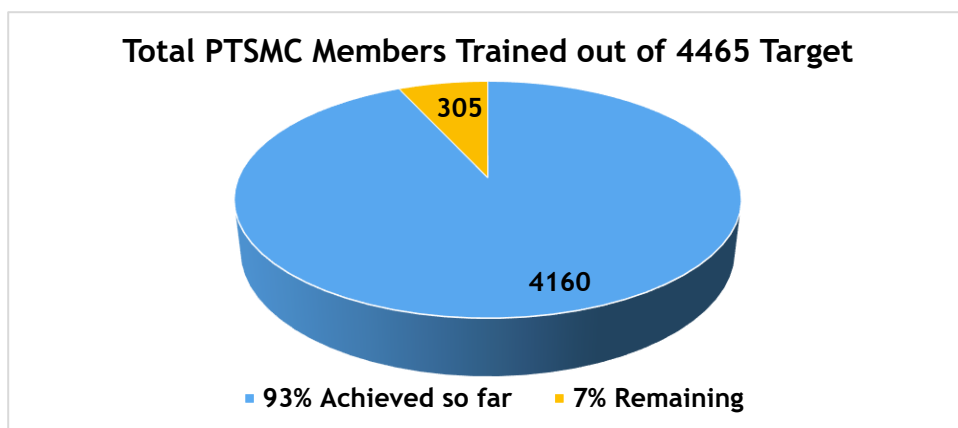

## 2.8. Number of teaching staff trained in the project specific schools

**Activity Updates:** The pie chart shows that 1796 of total target teachers have been reported trained so far. This proportionates to have achieved 90% of the total project target as per dashboard so far.

PMU has completed training of 1534 hired teachers which include 1308 JVT teachers and 226 EST teachers. 39 head teachers have been trained under the project.

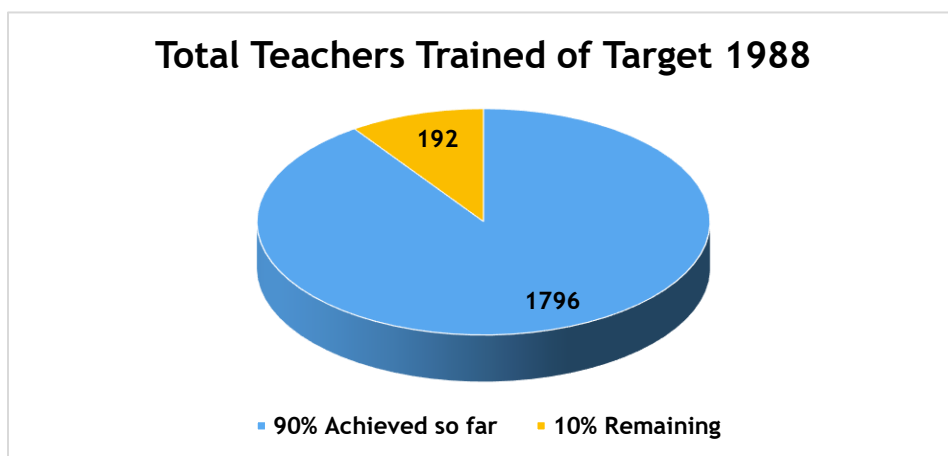

## 3.0. Detail table of the set target achievement against the result framework

Project Development Objectives	Target	Status	Remarks
Girls enrolled in grades K-5 of project supported government schools	26819	38366	143% Target achieved
Boys enrolled in grades K-5 of project supported government schools	15489	17942	116% Target Achieved
Student retention in project schools	75%	81%	108% Target Achieved ( the target has been calculated as of year two though these 303 schools have completed their first study session)
Girls enrolled in grades 6-10 of project supported government schools	1841	3127	170% Target Achieved

Intermediate Results			
Number of new primary schools established through community support	725	690	92% Target Achieved
Number of schools upgraded from primary to middle level	95	95	100% Target Achieved
Number of schools upgraded from middle to high/higher secondary level	25	25	100% Target Achieved
Number of government schools to which furniture (incl blackboard) is provided	845	743	88% Target Achieved
Number of schools to which TLM kits provided	845	790	93% Target Achieved
Number of government schools in which ECE program established	845	808	96% Target Achieved
Number of PTSMC members trained in targeted project schools	4465	4160	93% Target Achieved
Number of teaching staff trained in the project specific schools	1988	1796	90% Target Achieved
Project reports generated on selected indicators	11	11	100% Target Achieved

#### 4.0. Grievance Redressal Mechanism (GRM):

*Table B (detailed sheet attached as Annex-A)*

Summary of BEP-GRM Cases						
Description	Cases by Jul-Sep, 2018			Cases by Oct-Dec, 2018		
	Total Filed	Total Disposed of	Total Pending	Total Filed	Total Disposed of	Total Pending
*CRC/General Complaints	50	50	0	50	50	0
Court Cases	30	9	21	36	16	20
Procurement Cases	5	5	0	5	5	0
<b>Total</b>	<b>85</b>	<b>64</b>	<b>21</b>	<b>91</b>	<b>71</b>	<b>20</b>

*\*CRC/General Complaints include all the complaints submitted to confirm schools selection, NTS tests, and Teachers selection. Since CRC-Complaint Redress Cell is chaired by concerned division honorable Commissioner at Division level, PMU does not have any mandate to redress the cases falling under the CRC level specifically in regard to teachers selection. However, PMU GRM-PAC receives the complaints and guides the complainants to move to the CRC to file their complaint.*

### 5.0. ESMP Quarterly Progress Report Oct-December, 2018

Construction stage									
Balochistan Education Project Quarterly ESMP Implementation and Checklist Status									
S. No	District	Total Schools	Data Received during First quarter	Data Received during second quarter	Data Received during third quarter	Data Received during fourth quarter	ESMP Checklist Filled Construction stage	Key Findings	Remedial Actions Taken (if any)
1	Quetta	28	2	1	7	7	No environmental or construction related issue reported		
2	K abdullah	39	9	13	12	1	No environmental or construction related issue reported		
3	Mastung	19	0	18	0	0	No environmental or construction related issue reported		
4	Pishin	29	3	8	5	7	No environmental or construction related issue reported		
5	Awaran	21	2	1	4	7	No environmental or construction related issue reported		
6	Khuzdar	35	11	0	3	11	No environmental or construction related issue reported		
7	Kalat	25	3	1	12	4	No environmental or construction related issue reported		
8	Lasbella	54	14	14	8	9	No environmental or construction related issue reported		
9	Hernai	20	0	17	2	0	No environmental or construction related issue reported		
10	K saifullah	35	7	27	0	0	No environmental or construction related issue reported		
11	Sherani	20	2	12	2	0	No environmental or construction related issue reported		
12	Zhob	40	6	15	8	1	No environmental or construction related issue reported		

13	Ziarat	25	1	20	0	0	No environmental or construction related issue reported		
14	Barkhan	31	2	5	10	5	No environmental or construction related issue reported		
15	Kohlu	17	2	4	8	0	No environmental or construction related issue reported		
16	Loralai	30	0	8	16	2	No environmental or construction related issue reported		
17	Musakhail	27	0	16	5	0	No environmental or construction related issue reported		
18	Dera Bughti	32	1	10	0	0	No environmental or construction related issue reported		
19	Jaffarabad	28	4	23	0	1	No environmental or construction related issue reported		
20	Jhal Magsi	20	2	18	0	1	No environmental or construction related issue reported		
21	Kachi	20	2	11	0	0	No environmental or construction related issue reported		
22	Naseerabad	46	25	21	0	0	No environmental or construction related issue reported		
23	Sohbatpur	28	5	23	0	0	No environmental or construction related issue reported		
24	Sibi	19	3	4	1	1	No environmental or construction related issue reported		
25	Chaghi	30	11	0	14	1	No environmental or construction related issue reported		
26	Kharan	29	6	9	4	4	No environmental or construction related issue reported		
27	Noshki	25	14	6	5	0	No environmental or construction related issue reported		
28	Washak	19	3	13	0	1	No environmental or construction related issue reported		
29	Gwadar	25	0	0	0	9	No environmental or construction related issue reported		
30	Kech	26	0	0	6	6	No environmental or construction related issue reported		
31	Punjgoor	22	2	12	1	0	No environmental or construction related issue reported		

Total 78 construction stage checklists have been received during reporting quarter of 2018.

Operational stage								
Balochistan Education Project Quarterly ESMP Implementation and Checklist Status								
S. No	District	Total Schools	Data Received during First quarter	Data Received during second quarter	Data Received during third quarter	Data Received during fourth quarter	Key Findings	Remedial Actions Taken (if any)
1	Quetta	28	0	0	11	2	No issue reported	
2	K abdullah	39	0	0	7	0	No issue reported	
3	Mastung	19	0	0	10	4	No issue reported	
4	Pishin	29	0	0	10	9	No issue reported	
5	Awaran	21	0	0	0	11	No issue reported	
6	Khuzdar	35	0	0	0	4	No issue reported	
7	Kalat	25	0	0	3	6	No issue reported	
8	Lasbella	54	0	0	0	9	No issue reported	
9	Hernai	20	0	0	3	6	No issue reported	
10	K saifullah	36	0	0	35	0	No issue reported	
11	Sherani	20	0	0	3	0	No issue reported	
12	Zhob	40	0	0	14	10	No issue reported	
13	Ziarat	25	0	0	15	2	No issue reported	
14	Barkhan	31	0	0	8	6	No issue reported	
15	Kohlu	17	0	0	3	10	No issue reported	

16	Loralai	30	0	0	1	13	No issue reported	
17	Musakhail	27	0	0	4	0	No issue reported	
18	Dera Bughti	32	0	0	8	4	No issue reported	
19	Jaffarabad	28	0	0	0	10	No issue reported	
20	Jhal Magsi	20	0	0	0	6	No issue reported	
21	Kachi	20	0	0	12	0	No issue reported	
22	Naseerabad	46	0	0	0	46	No issue reported	
23	Sohbatpur	28	0	0	27	1	No issue reported	
24	Sibi	19	0	0	7	1	No issue reported	
25	Chaghi	30	0	0	11	4	No issue reported	
26	Kharan	29	0	0	8	12	No issue reported	
27	Noshki	25	0	0	16	0	No issue reported	
28	Washak	19	0	0	6	13	No issue reported	
29	Gwadar	25	0	0	0	0	No issue reported	
30	Kech	26	0	0	0	0	No issue reported	
31	Punjgoor	22	0	0	0	0	No issue reported	

**Total 189 schools of BEP have been operationalized by reporting quarter of 2018.**

### Status of completion of ESMP remedial actions

.No	District	Region	ESMP Checklist Filled Siting stage	Key findings	Remedial Action taken (If any)	Current status	Estimated Cost
1	Quetta	1	GGPS Killi Mehrab khan Kuchlak	Transmission lines are passing near the boundary wall of a school.	Keeping in view the location of transmission lines the building is planned on the opposite site of a school building which is safe for the construction. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security.	Transmission line has been covered with rubber casing to ensure child safety	Rs. 200000/-
2	Quetta	1	GPS Shaheed Aymal kasi	Adjacent to solid waste dumpster	Members of PTSMCs have been contacted to remove waste from the school site.	School gate has been provided from the other side. However PTSMCs members have been motivated to remove waste from nearby area of school	
3	Quetta	1	Shin Kach Hanna	Near Flood pathway	Trench will be made to divert flood water	completed	Rs.20000
4	Quetta	1	GGPS Gulshan Hassan	Transmission line is passing over the school site.	Concerned department has been contacted and it was told that the transmission line is (HT) and it cannot be replaced.	HT line cannot be replaced	
5	Quetta	1	Zarat Colony	Transmission lines are passing over	Relocation of transmission line is underway with the concerned department. In case it doesn't get final then	Pole has been filled with mud	



				the selected site	the transmission lines will be covered with the rubber pipe to ensure children safety.		
6	Pishin	1	Shin Kantay zai	Site situated in flood pathway	Retaining wall will and land levelling required.	Completed	Rs.400000/-
7							-
8	K Abdullah	1	GPS Killi Haji Abdul Manan Toba	School site is located on top of hill	Land levelling is required	Completed	Rs.60000
9	K Abdullah	1	GPS Killi Mohammad Yousaf Azadzai Dobandi	Disputed land	Relocation of school site is under discussion	New site has been finalized	-
10	Lasbela	2	Madina Colony	Transmission line is passing over the selected site.	Relocation of transmission line. Low Transmission Line (LT) but the wires are very high and casing cannot be put on them. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security.	Pole has not been taken out of school building but for the safety of school children pole has been filled with mud.	Rs. 200000/-
11	Lasbela	2	Jam Yousaf colony	Electricity wire of a home is passing over boundary wall of school building.	Relocation of electricity line or put casing on the electricity wire. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security.	Electricity wire has been shifted	

12	Lasbela	2	Pathar Colony	Site is located near flood pathway	Stone pitching wall is proposed to safe building from flood water.	Completed	Rs.500000/-
13	Lasbella	2	GGMS Kumacha	This school is adjacent to river and fall in a flood pathway.	A retaining wall to control flood water has been incorporated in school plan to provide safe environment for the students.	Completed	Rs.1000000
14	Khuzdar	2	GGMS Khairawa	Electricity wire of a home is passing over the school site.	Relocation of electricity wire or put casing on the electricity wire. Incase electricity wire is not relocated then the pole will be filled with mud and electricity wire will be covered with rubber casing to ensure child security.	Electricity wire has been shifted for the safety of school children	
15	Zhob	3	GGPS Shahbzai	Transmission lines are passing over the selected site	Relocation of transmission line is underway with the concerned department. In case it doesn't get final then the transmission lines will be covered with the rubber pipe to ensure children safety.	Discussion with concerned department is underway.	Rs. 200000/-
16	Ziarat	3	GGPS Kan depot.	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed	Rs.10000/-
17	Ziarat	3	GGMIDS Pitao Zindra	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed	Rs.10000/-
18	Ziarat	3	Poi Shareef	Transmission line is passing in school building	Relocation of transmission line. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will	Concerned department has been contacted for the relocation	Rs.10000

					be covered with rubber casing to ensure child security.	of transmission line.	
19	Barkhan	3	Rakhni City near Wapda Grid station.	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Traffic sign board has been installed	Rs.10000/-
20	Barkhan	3	GGPS Bagra Badiani	Transmission line is passing over the school site.		Electric wires have been covered with rubber casing	
21	Kachi	5	GGPS Muhallah Muhammad Ali Meerzai Abad	Transmission lines are passing over the selected site	Relocation of transmission line is underway with the concerned department. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child safety.	Not Yet completed	Rs. 200000/-
22	Sohbatpur	5	GGPS Siandad Kanrani	The school site is close to dumpster	DFP of concerned district has been contacted to relocate the dumpster.	Not Yet completed	-
23	Sibi	5	Elementary College	Transmission line is in school building	Relocation of transmission line. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security.	Transmission line can't be relocated but casing will be put on the wires for the safety of school children	Rs.40000/-

24	Naseerabad		GGMS Ghulam Muhammad Sarpara	Close to solid waste dumpster		Waste has been removed from the site	
25	Washuk	6	GPS Killi Gohari Mir barkat mulazi	Electricity wire is passing over the school building	Relocation of electricity wire. In case the electricity wires are not relocated then the wires will be covered with rubber casing to ensure child security.	Electricity wires have been relocated	
26	Gwadar	7	Senator Ishaq	Transmission line is passing from the school building,	Relocation of transmission line. Incase transmission line is not relocated then the pole will be filled with mud and transmission lines will be covered with rubber casing to ensure child security.	Transmission line is not yet relocated	Rs. 200000/-
27	Gwadar	7	GGPS Zahar Bahar	Site adjust to Highway	Traffic sign to be installed	Not yet completed	Rs.10000
28	Kech	7	PS Nokabad Hoshab	The school site is close to highway	A traffic sign indicating school is close will be installed on the highway at the visible place.	Not yet completed	Rs.10000/-

Balochistan Education Project ( BEP ) Grievance Redressal Sheet by Jul-Sep, 2018								
Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	03-Jan-16	Jamila Hassan	Nawa Kili Quetta 0304-3324241	Complaint application was submitted regarding NTS merit list UC Nawa kili	—	Yes	Complainant wanted to exclude ADE marks of qualified candidate. Her request was rejected by District Recruitment Committee as not valid. In recruitment policy issued by Education Department, ADE marks is applicable.	It is against Recruitment Policy notified by Education Department
2	02-May-16	Sain Dad	Sohbatpur Ghot Sain Dad kandani	Submission of letter (Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list.	03-05-16	Yes	The complainant wanted District Recruitment Committee to consider her candidate in lieu of provision of land. However, the Recruitment in the project is made through merit based recruitment policy as notified by Education Department. Therefore, complaint was rejected and recruitment is made on merit based only.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
3	2nd May-2016	Wali Dad	Qaisarabad Sohbatpur 0343-3788221	Complaint application was subjected regarding unfair recruitment of teacher, for he has devoted land for school and wants his candidate to be short-listed for his UC.	2nd May-2016	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
4	22-Jun-16	Bilqees D/o Nabi Dad	Lasbela UC Liyari	(JVT complain application was submitted) Complain application was regarding discrimination objection on NTS criteria	22-06-16	Yes	Applicant was ineligible because she is not Intermediate pass (which is basic qualifying criteria for teachers) and also she didn't qualify NTS test.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
5	22-Jun-16	Maryam D/o Muhammad Siddique	Lasbela UC Uthal	(JVT complain application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted.	22-06-16	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.
6	22-Jun-16	Rehana D/o Yar Muhammad	Lasbela UC Uthal	(JVT complain application was submitted) In application it is stated that the community had devoted land for school on one condition iff their candidate be shortlisted.	23-06-16	Yes	The complaint was rejected by District Recruitment Committee as his candidate is not on merit. Recruitment is made on merit basis in concerned union council.	Recruitment of teacher is made on merit basis only, as per notified policy by Education Department.

7	24-Jun-16	Sumaira D/o Abdul Hakim	Lasbela UC Winder	Complain application was regarding discreamenative objection on NTS criteria	24-06-16	Yes	—	Applicant was not elligible because she is not FA and also she didn't qualified NTS test.
8	25-Jun-16	Samiya Khair D/o Khair Muhammad	Rehmdwa Noshki	(JVT complain application was submitted). Objection on merit list finalized by District Recruitment Committee.	07-07-16	Yes	District Recruitment Committee considered her request and issue is resolved.	—
9	26-Jun-16	Saima D/o Din Muhammad	Lasbela UC Lakhara	(JVT complain application was submitted ) she claims though she has done metriculation but is not shortlisted in NTS merit list.	26-06-16	Yes	Required qualification intermediate. She is matriculate thus District Recruitment Committee rejected her complaint.	Applicant was not elligible as per approved criteria
10	27-Jun-16	Saqiba D/o Abdul Razzaq	Loralai UC Zingewal Kotazai	(JVT complain application was submitted). Complain was stated regarding rectification of UC	24-11-16	Yes	District Recruitment Committee has verified the documents of candidates and issue was resolved	—
11	28-Jun-16	Raj Bibi D/o Muhammad Ali	Lasbela UC Uthal	(JVT complain application form was submitted) She claimed that her B.Ed and M.A degree was not considered while finalizing NTS merit list.	05-07-16	Yes	District Recruitment Committee Lasbella considered her applicabtion and it was resolved on merit. She is on 7th number in merit	—
12	28-Jun-16	Mehbooba D/o Paida Khan 0334-2811516	Kili Saghri Loralai.	Mrs. Mehbooba compliants, that she has secured 50 marks whereas in merit list she has given only 43 marks.	24-11-16	Yes	Issue resolved by District Recruitment Committee, on the basis of complaint merit list were checked and made correction in the numbers of the complinant.	—
13	29-Jun-16	Sakina Bibi D/o Aziz Khan	Loralai UC Zangewal	Mrs. Sakina bibi complianed that she has passed NTS test but her name is missing in merit list.	24-11-16	Yes	Issue is resoolved, as on the basis of her complaint the merit list was tallyed and and found that her name was missing due to non-availability of her documents, but on submission/persentation of complete documents her name was included in revised merit list.	—

14	30-Jun-16	Razai Taj D/o Abdul Ghani	Loralai UC Ponga	C.T and B.A marks were not included in NTS merit result.	24-11-16	Yes	Case was forwarded to District Recruitment Committee and requested to include her CT and BA Marks, District Recruitment Committee verified her documents and included her marks in the merit list.	—
15	04-Jul-16	Razia D/o Yar Muhammad	Lasbela UC Winder	The candidate has declared the test and is rejected for her qualification is metric and other candidate from other UC is selected.	15-07-16	Yes	She is Matriculate only and does not meet eligibility criteria and therefore was not shortlisted and if no candidate is selected on UC level then on tehsil level candidate will be selected.	Required qualification for JVT post is intermediate with 2nd division.
16	04-Jul-16	Gul Bushra Kakar D/o Abdul Ghafor	Loralai UC Ponga	(JVT complain application was submitted) B.A and ADE marks not included	01-11-16	Yes	Issue resolved by District Recruitment Committee , the case was forwarded to District Recruitment Committee and requested to included her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract.	—
17	07-Jul-16	Hameeda D/o Muhammad Farooq	Loralai UC Ponga	Complain was stated regarding rectification of UC	24-11-16	Yes	Issue resolved by District Recruitment Committee, On the basis of her complaint, Locals of other candidates were checked and found that on candidate were not belonging to here UC and excluded all the candidates from merit list who were not belonging to the same UC.	—
18	11-Jul-16	Shahida D/o Jumma Khan	Lasbela UC Wayara	(JVT application was submitted) The community had devoted land for school on one condition iff their candidate be shortlisted and a candidate from other UC is shotlisted.	21-07-16	Yes	Firstly she did not pass NTS test secondly if no candidate is selected on UC level then on tehsil level candidate will be selected.	District Recruitment Committee rejected the complaint because it is not in recruitment policy



19	29-Jul-16	Gulshan W/o Noorullah	Lorlai UC Thal	Higher education marks are not included in NTS merit list.	25-11-16	Yes	Issue resolved by District Recruitment Committee , the case was forwarded to District Recruitment Committee and requested to include her BA marks, District Recruitment Committee checked her documents and included BA and ADE marks as a result she secured 2nd position and got contract.	—
20	01-Oct-16	Khan Meer	Zhob UC Wala Akram	The UC topper Ms.Farzana Zareef does not belong to UC Wala Akram but to UC Omzha( Rectification of U.C)	14-10-16	Yes	Case resolved by District Recruitment Committee on 24-Dec-2016,	—
21	01-Nov-16	Gulshan Bibi D/o Abdul Khaliq	Qila Saifullah UC Sadar Muslim bagh	It was stated in complain that her B.Ed marks were not included in merit list.	01-12-16	Yes	Issue was addressed to District Recruitment Committee. Marks added as per documents provided	—
22	01-Nov-16	Fatima Bibi D/o Hassan Khan	Qila Saifullah UC Bandad Mir zai	Complain was stated regarding rectification of UC	01-12-16	Yes	UC Rectified by District Recruitment Committee as per documents	—
23	01-Nov-16	Zarmina Kakar	Qila Saifullah UC Sadar Muslim Bagh	Objection on ADE marks separately.	01-12-16	Yes	Issue was addressed by District Recruitment Committee.	—
24	03-Nov-16	Binish Kanwal	Quetta ,Kechi Baig	Complaint for JV teacher's recruitment. She claimed her name is not included in merit list.	3rd Nov-2016	Yes	Ms.Binish Kawal is included in merit list on 78th number , her total obtained marks are 57.25, her basic qualification is B.A because her F.A was scored in 3rd div.	—
25	03-Nov-16	Fatima D/o Pehlwan	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated for her B.A marks were not included in NTS merit result.	01-12-16	Yes	Issue was addressed to District Recruitment Committee. Marks added as per documents provided	—
26	04-Nov-16	Sadiqa D/o Nadir Khan	Qila Saifullah UC Sadar Muslim Bagh	B.Ed and Physical education marks are not included in NTS merit result.	04-11-16	Yes	Issue was addressed to District Recruitment Committee. B.E.d Marks added as per documents provided, But physical education can't be added because they are not relevant .	—
27	04-Nov-16	Mir Alam Shahwani	Quetta 0333-7812784	Complaint was recorded regarding NTS result. Ms.Rahila Rahim had her B. Ed degree with her and is not short listed.	05-11-16	Yes	DRC considered her request but she is on 85th number in merit	PTC Percentage has been given instead of B.Ed according to policy. And she is on 85th in merit list.

28	04-Nov-16	Khair un Nisa	Qila Saifulla UC Sadar Muslimbagh	Rectification of merit list (The Qualification marks were not included in merit list)	01-12-16	Yes	Marks got added in meirt, Rectified by District Recruitment Committee	—
29	04-Nov-16	Sardar Bibi & Dowlat Bibi	Qila Saifulla UC Bandad Mirzai	Complain was stated regarding rectification of UC	01-12-16	Yes	Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee	—
30	05-Nov-16	Gul Sumaira D/o Qalandar Khan	Zhob UC Meena Bazar	Objection on not including B.A marks in NTS merit result.	24-12-16	Yes	Issue resolved by District Recruitment Committee . Marks added as per documents provided.	—
31	11-Nov-16	Razia Gul D/o Haji Muhammad Syed	Qila Saifullah UC Sadar Muslim Bagh	Complain was stated regarding rectification of UC	02-12-16	Yes	Candidate added in her UC as per her Local/residential certificate. Rectified by District Recruitment Committee	—
32	11-Nov-16	Froza Khanum	UC Narezai	Complain application was regarding NTS merit list	24-12-16	Yes	Candidate were informed about final merit as per NTS result and District Recruitment Committee working. issue resolved by District Recruitment Committee	—
33	2nd Dec- 2016	Muhammad Rafique	Musa Khail 0335-7418858	Complaint was submitted on subject of school selection. He claimed that the selected school in his town is located on 50 meters only while the school they applied for is located on 2 km distance and the enrolment of students too is more than the selected school .	27th Dec- 2016	Yes	On this complaint, PMU has formed a committee of SMIP team and sent to re-visit the selected site (Killi Dargai hassankhail) and committee reported that there is no government school at the distance of 02 Km from the site. A report with GPS coordinates has been verified by SMIP team.	—
34	26th Dec- 2016	Abdul Sattar	Zhob 0313-8820907	Complaint application was submitted regarding Final Merit list of NTS test for JVT, his candidate Ms. Ameer Bakhta was 3rd in the list though she had her PTC degree with her and the candidate who was at the 2nd number had no PTC degree but that candidate had higher marks in NTS.	26th Dec- 2016	Yes	His case was dealt by Naseebullah ( M&E Manager), Jahanzeb Nasar( Legal Officer) and Kulsoom ( Program Associate). The team listened to his complain and was explained the recruitment policy in detail , the complainant was satisfied then.	—

35	28th Dec-2016	Abdul Aziz	Washuk 0336-3959675	Submission of letter ( Subject: Cancellation of land mutation) for his candidate was not shortlisted in NTS merit list.	2nd Jan-2016	Yes	The case has been resolved the land mutated	Resolved.
36	30th Dec-2016	Khaliqdad	Muslim Bagh 0335-2700714	In advertisement the U.C for which candidate Ms.Khair un Nisa was shortlisted was Sultan Zai but actually the school is situated in Sara Gharh U.C, so Mr.Khaliqdad came to discuss the case with concern officer, for officer was not available so Naseebullah ( M&E Manager) dealt.	21st Feb, 2017	Yes	Babar Jaffar ( E.O) dealt the case and complainant was told that letter is sent to DC for verification of UC , as soon as UC is verified he shall be informed by BEP team. After Final merit got signed, DRC received several complaints against merit regarding UCs issue. This issue is highlighted under DRC which is being addressed. The revised final merit will be signed in coming week.	—
37	12-Mar-17	Tayyeba Rasheed 5310342662581	Kachhi Bolan	The complaint was received via e.mail . There was mentioned that the candidat Ms.Tayyeba Rasheed had applied for the post of JVT for a school in 2013 but she was not selected and there were 3 posts vacant and only one candidate was selected . As two posts are vacant so BEP should assign the vacant post to the above mentioned candidate.	13th March 2017.	Yes	The complain was discussed with Abdul Qayyum (Program Assistant) called the candidate and talked to her husband and told the complainant that this case belongs to PGEB project which is afterwards handed over to Government, so the Complaint should submit his request to Education Department but he(The candidate's husband) was rudely denying the fact and said that if your project will not facilitate us then i will go to world bank against you people.	Resolved.
38	15-Mar-17	Muhammad Naveed	Barkhan 0333-7736238	The complain was received via text on our official contact number, there was stated that the applicant Muhammad Naveed has appeared in test for ( MonitoringAssociate) in RTSM PMC on 20th Nov-2016 and he also appeared in interview on 13th Dec-2016 but still has no clue about final selection.	15-Mar-17	Yes	The complain was discussed with Ahsan Jamil ( HR officer) , the candidate is on waiting list said HR Officer.	Resolved.

39	17-Mar-17	Sorab Khan 55202-146312-5	Kohlu 0331-8031145	The complainant visited BEP head office and recorded his complain to Mr.Naseebullah (M&E Manager), the complain gist was regarding school selection in Kohlu district, the school application form was submitted on 25th Feb-2016 and applicant name was Jamal Khan ( village : Kili Darwaish abad Tamboo) but his application was not shotlisted and the BEP team selected a nearby town while both the application was submitted on same date.	17-Mar-17	Yes	The case was dealt by Naseebullah ( M&E Manager) and Latif Marri (E.O) , they explained to him that the other application was selected for there are more enrollement of students than that of his recommended town, google map was shown to him and the BEP team made him convinced that the students of his town can also go to the selected school easily.	Resolved.
40	20th-March-2017	Saleh Muhammad District Member Nakas 2	Hernai	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliaz pedri and killi raza muhammad. He claimed that these Schools belong to unin council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrug.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
41	20th-March-2017	Muhammad Ramzan S/o Amir Muhammad	Hernai, UC Nakas2	The Complainant had an objection on the placement of Schools in the incorrect UC, i.e. Killi Paliaz pedri and killi raza muhammad. He claimed that these Schools belong to unin council Nakas 2 but in NTS Test these are shown in Nakas 1. one post which belonged to Murgha Tangi Sar , it belongs to Union Council Nakas 2 but it is shown in Shahrug. Further more two candidates Miss Nahida Tareen and Miss Sumayya Tareen are of other UC but these candidate names have been included in Nakas 2 U.C.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
42	20th-March-2017	Esmatullah S/o Nasrullah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.

43	20th-March-2017	Muhammad Salim S/o Haji Muhammad Siddique	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
44	20th-March-2018	Khair Shah S/o Syed Nadir Shah	Hernai, UC Nakas2	The complainant had objection that (i) Ms.Nahida Tareen and Ms. Sumayya Tareen who are listed as candidates of Nakas 2 U.C don't belong to this U.C. (ii) Kili Muhammad Raza and Kili Paliaz Pedri are located in Nakas2.	18-04-2017	Yes	UC Corrected, Merit got final	Resolved.
45	27-Mar-17	Sultana D/o Rakhal Shah	Qalat	Guidance required teacher recruitment under BEP, Community members Khadi Bangalzai has submitted Complain against Bibi Samina D/o Jalal Khan. She has changed her local certificate from Municipal Corporation to Union Council of Kalat.	District Recruitment Committee will take decision.	Yes	action taken against complain and she has recomended agaiNST vacant post, approval has also taken by secretary education.	—
46	3rd-Apr-17	Naeem Shah S/o Haji Abdul Kareem 54400-0509307-3	Ziyarat Sanjavi 0345-8326567	In his application it was stated that his candidates who actually belong to U.C "Poi" but in NTS result which was held on 24th Jan-2017 the candidates are included in UC "Kach", He wants their names to be listed for U.C "Poi" where they really belong from.	Case is forwarded to DRC .	Yes	Case was addressed to DRC by Education Officer Babar Jaffar. And DRC listed their names for U.C Poi.	—

47	18th April-2017	Duniya Khan S/O Shiney Gul 56201-1770383-9	Muhammad Rafique, Alghouri Boot House, Wasey Market Killa Saifullah	it is stated in the received document that the village kiili Touda Ghazgai Ghorezai killa saifullah is selected for establishing a school as per the need of the area. As the natives are ready to facilitate Balochistan Education Project by providing Female candidates and any kind of support so it is requested to the Project Director to please do not cancel the school for the sake of the Education and future of the local kids.	16-05-17	Yes	Annanounced NTS for 3 times, but teacher didn't found in the UC. Other UC /tehsil Teacher can't perform there duties as the area is flung from city. As per discussion with Manger Education, the site is tempoararly dropped. Will go for male option, if having less than target schools in district.	Resolved.
48	12th April-2017	abdul Qadir S/O Allah Dinah 53302-2090922-9	Abdul Qadir S/O Allah Dinah, Nafoorullah Dinah, Majeedana Magsi, Tehsil and District Jhal Magsi.	The Complainent says that I have donated land for the establishment of Schools to Government of Balochistan Secondary Education Department after the selection of site and as promissed by the representatives of BEP one post was to be nominated from my family in return to the land and rooms i gave to government but BEP did not recriut my candidate after NTS Test.	12th Apl-2017	Yes	—	District Recruitment Committee rejected the complaint because it is not in recruitment policy and no hiring has take place yet in said village.
49	19th-04-2017	did not provide his personal information due to Tribal Affairs at their village. Only phone No. is provided i.e. 03337935647 , UC LOTI, District Dera Bugti.	3337935647	There were three applicants who had submitted the grivience that instead of their deserving sites namely ; 1. Killi Dr Saifuddin Shambani, 2. Killi Noor Muhammad Shambani, and 3. Kiili Pehelwan Shambani another three sites were selected for schools i.e. 1. Killi kehlani UC Loti, 2. Goor Shamool UC Loti, and 3. Phogani UC Loti. They have appealed for Justice to Worthy Project Director.	25-Apl-2017	Yes	—	The applicant was contacted to provide justification to the decision taken by PMU regarding school selection criteria however the applicant did not respond. It must be noted that the District wise target of Dera Bugti was 23 and the sites were finalized on the basis of Enrolment, Distance from next level and security where construction could be executed. The said Union Council is one of the disturbed areas where project activities may not be possible to conduct.

50	17th-04-2017	Sania Jalal D/o Mir Jalal Khan 51202-1521900-6	U.C Pandran, Tehsil Kalat, Kalat.	Complain was received via TCS. She is on 2nd No. in UC and affidavit of being Rejected as candidate on third no. in Union Council Miss Bibi Sultana has submitted complaint against her for changing her UC from MC Kalat to Pandran.	Case is already in DRC	Yes	case is rejected by DRC	The local certificate was made after due date of advertisement.
----	--------------	---	---	---	------------------------	-----	-------------------------	---

### Court Cases (Mohtasib, Honourable High Court and Honourable Supreme Court)

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	08-Nov-16	Mashoor Bibi	Jaffarabad	Complain was submitted regarding teacher recruitment. (Case against PGEB recruitment process)	Hearings to be fixed by the Hon'ble Supreme Court of Pakistan	Case Subjudised before the Hon'ble Supreme Court of Pakistan	Case pertains to PGEB project and review application is under trial in Honourable Supreme Court of Pakistan. Mr. Haroon DS (Judicial) Education Department has attended court on behalf of Education Department and project in Islamabad on 17-11-2016.	Pending
2	8th Dec-16	Zahidullah Khan s/o Zarif Khan VS SHO Police Station Hub and others	Lasbella Gulshan Colony Tehsil Hub	A Complaint was recorded before the Hon'ble High Court of Balochistan that the land gifted and dedicated for school which was supposed to be built by PGEB has been confiscated. Therefore, the Hon'ble Court through Order Dated 8.12.2016 in a case called Zahidullah Khan VS SHO Hub and others (Criminal Miscellaneous Quashment No 111 of 2013), deputed the Legal officer of GPE to visit the site and take over the possession of the said land with the help of SHO, Police Station Hub, and the Revenue staff.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 07 December 2018	yes	The land has been officially transferred in the name of "Secondary Education Department, Government of Balochistan". The details of the area of the land as well as the exact location of the land has been recorded on the mutation (Fard) document. The Revenue Record in the office of Tehseel, at Tehsil Hub, District Lasbella has been updated to this effect and the mutation document has been acquired. A new primary school is being proposed under BEP project	Case Resolved



3	20-Dec-16	MS. Shahina /Do Noor ur Haq	Qila Saifullah	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining second position in entry test, she still was not considered for the job by PGEB authorities.	The case has been argued before the Hon'ble Ombudsman (Mohtasib) Secretariate Balochistan, Quetta, and is awaiting for the Judgment to be announced by the Hon'ble Secretariate	Judgment Pending	Mr. Jahanzaib Nasir legal Officer argued the case before the Hon'ble Ombudsman, Balochistan, and the written Judgment is awaited	Pending
4	22nd Feb-2017	Wadera Nihal Khan	Dera Bogti	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection.	Two written replies from the GPE-BEP have been submitted on 11th May 2017 as well as on 07th March 2017, and the disposal of the matter is still pending.	Disposed of as being withdrawn by the Complainant. Whereas, the official finding from the Hon'ble Ombudsman still awaited	The Formal intimation of the withdrawal of the Complainant is still awaited	Disposed off
5	22nd Feb-2017	Bashiran Bibi	Jaffarabad	Petition submitted before Honorable Supreme Court of Pakistan, regarding teacher recruitment,	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble Supreme Court of Pakistan.	Pending
6	20-Mar-17	Akhtar Shah Mandokhail	Zhob	complaint submitted before the Hon'ble Ombudsman, Balochistan, Quetta. The Complain complaint pertains to be against the recruitment of the Teaching staff. The copy of the complaint and the Notice from the Hon'ble Ombudsman Secretariate has been received recently (19th July-2017) and the Legal Officer has appeared before the Authority and waved off the notice. the reply to the complaint along with the relevant supporting documents will be submitted in due course.	NA	Judgment Pending	Pending	—

7	28th Mar-2017	Haji Muhammad Azeem Khan and Sons	Qilla Saifullah	Legal Notice from "Mr Iqbal Ahmad Kasi Advocate Law Firm", on behalf of Haji Mohammad Azeem Khan and Sons was received in dispute over Procurement for different packages including construction /Rehabilitation of schools (12 Primary and 1 Middle) in Balochistan.	10th Apl-2017	Yes	The Legal Notice has been replied in writing, and sent the reply through TCS Courier on Dated 10th April 2017 and the matter had then been settled and resolved.	Resolved.
8	5th Apl-2017	Sahib Zadi D/o Mir Khan	Barkhan	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as EST.	A written reply from the GPE-BEP has been submitted on 30th March 2018 and the matter was disposed of mainly on the grounds argued in the same reply	Complaint is Dismissed on 15th August 2018, pursuant to the Letter bearing Number 168/2018/PMS /01024523, Dated 20 August 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	Complaint is Dismissed on the grounds that the Complainant did not fulfill the criteria of becoming as an "EST" teacher as per policy laid by the Education Department.	Disposed off.

9	23rd Apr- 2017	Sehrish David D/o Jhon David	Nawa Killi Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding JET teacher against Daughter Quota...	the complaint, after being prproperly written replied by GPE-BEP on 06th April 2018, has been disposed off by the Hon'ble Ombudsman on the terms that the Applicant has to approach the proper forum	Complaint is Diisposed of on 11th april 2018, pursuant to the Letter bearing Number 720/2018/PMS /510-12, Dated 13 April 2018. The Complainant has been referred to present their case before the Secretary Education who would e in a better position to address the matter. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	Complaint is Dismissed on the grounds that the Complainant has to approach a proper forum.	Disposed off
10	21-Jun- 17	Bibi Rehana	Ziyarat	Constitutional Petition No 653 of 2017 has been submitted before the Hon'ble High Court of Balochistan, Quetta, on 21st June 2017 by the two Petitioners namely Bibi Rehana and Bibi Rakia against the GPE-BEP along with the Education Department, Government of Balochistan, the Deputy Commissioner and the District Education Officer of the Ziarat District, whereas, the Notice from the Hon,ble Court has been received recently on 17 july 2017. The matter pertains to be against the recruitmrnt of the female teacher in the area. the Legal officer has appeared before the Hon'ble Court and wave off the notice.	NA	Judgment Pending	Pending	—

11	08-Jul-17	Nasrullah S/o Allahdad	Musakhail	Notice has been received from Hon'ble High Court of Balochistan from Nasrullah Son Of Allah Dad, gist of grievance is not mentioned as yet, hearing is on 21st December 018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 17 December 2018	Pending	Pending	Pending
12	17-Aug-17	Tahira Bibi D/o Allah Dina	Jhal Magsi	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP have been submitted on 24th August 2017 and the matter was disposed of mainly on the grounds argued in the same reply	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at her case on merit. The official finding from the Hon'ble Ombudsman has been received pursuant to the Letter bearing Number 293/2017/PMS /Jhal Magsi/755-56, Dated 08 November 2017	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at her case on merit	Disposed off.
13	21st Aug-2017	Samad Khan Saqi S/o Ab.Hameed	Samad Khan Saqi and Brothers Zhob Ph:03112121812 Mob:032088603 93	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 15 Middle) District Sherani of Package/Activity No 50	Two written replies from the GPE-BEP have been submitted on 27th September 2017 as well as 19th March 2018, and the disposal of the matter is still pending.	Judgment Pending	Pending	

14	21st Aug-2017	Abdul Qayyum S/o Haji Habibullah	Afghan construction company Zhob Mob:03412882884	the applicant, before the Hon'ble Ombudsman, Quetta, has challenged the Bid for procedure conducted by GPE-BEP, Dated 19th June 2017 at 11:00 am for Construction/Rehabilitation of School (Primary, 12 Middle) District Zhob, Qamardin of Package/Activity No 48	A thorough written reply from the GPE-BEP has been submitted on 27th September 2017, and the matter was disposed of mainly on the grounds argued in the same reply	Disposed of as being withdrawn by the Complainant, the Complainant was assured by the GPE-BEP to look at their case on merit. The official finding from the Hon'ble Ombudsman has been received pursuant to the Letter bearing Number 399/2017/PMS /Zhob/493-94, Dated 026 February 2018. The official finding from the Hon'ble Ombudsman has been received and has been kept as record	The Complaint was submitted on 01 August 2017, and the written reply was submitted by the GPE-BEP on 27 September 2017	Disposed off
----	---------------	----------------------------------	--	---	--	---	--	--------------

15	26th Sep-2017	Hajira D/o Karim Baksh	Kech	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment. The complainant asserted in her application that despite obtaining 1st position in entry test, she still was not considered for the job by DRC.	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman on the terms that the Applicant has to approach the proper forum	Complaint is Dismissed on 15th August 2018, pursuant to the Letter bearing Number 168/2018/PMS /1024-25, Dated 20 August 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	The Complaint has been disposed off (Dismissed) by the Hon'ble Ombudsman on the terms that the Applicant has no Associate Degree in Education (ADE), hence the same was dismissed	Disposed off
16	09th Oct-2017	Saima D/o Nasir	Khuzdar	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Khuzdar Balochistan, there was filed a complain with the averment that the recruitment committee of DRC Sikanda abad Tehsil Sorab objection on merit list and pointed out that non inclusion of name in merit list and appointed another candidate who belongs to another district.	Pending	Yes	the complaint has been received on 09th October 2017 and since then has not been pressed any further	Pending

17	13-Oct-17	Saadiqa Bibi D/o Niamatullah	Muslim Bagh	A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment that the candidate is the resident of the village (Zharhi Muslim Bagh) and has passed NTS test despite that candidates from other far situated villages are hired for the posts advertised.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 30th May 2018. On 24th of October 2018, the final arguments have been given before the Bench headed by the Hon'ble Chief Justice of Balochistan. Whereas, the case has been reserved for final Order to be announced soon.	Pending	Pending	Pending
18	26th Oct-2017	Zar Khatoon	—	Notice has been received from Hon'ble High Court of Balochistan from Zar Khatoon, gist of grievance is not mentioned as yet, hearing is on 21st Aug-2018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 1st November 2018	Pending	Pending	Pending
19	26th Oct-2017	Bibi Rehana D/o Shah Buzerg Rakkia D/o Abdul Sattar	Ziyarat	A Complaint was recorded before the Hon'ble High Court of Balochistan regarding teacher recruitment, the petitioners claim that the abundant building in Killi Zargai UC Spezandi Tehsil district Ziyarat which is going to be functional via BEP so new vacancies must be created for the said school.	19th Oct-2017	Yes	the Petition was disposed off Dated 19 October 2017, on the terms that the School will be handed back over to the GPE-BEP, who then will functionalise the school and hand over the appointment letters to the two Petitioners	Disopossed off



20	1st Nov-2017	Shah Gul S/o Shadi Gul	Musa Khail	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding school site selection.	Two thorough written replies from the GPE-BEP have been submitted on 24th August 2017 as well as on 12 February 2018, and the disposal of the matter is still pending.	Pending	Pending	Pending
21	21st Nov-2017	Kaleemullah	Sun rise solar system Company.	Legal Notice from "Niamatullah Batezai Law Firm", on behalf of Mr Kaleemullah was received in a dispute over Procurement for scheme of 10 KV solar system for schools in Balochistan.	—	Yes	The same Legal Notice has been replied in detailed and comprehensive manner in writing and posted on through TCS Courier on Dated 21st November 2017	Replied
22	26th Dec-2017	Rabia Kakar D/o Abdul Hmeed	Loralai	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Loralai Balochistan, regarding JVT teacher recruitment.	Pending	Yes	Two written replies Dated 09th January 2018 submitted in person as well as reply Dated 06th April 2018 despatched through Courier has been submitted and the outcome is still awaited	Pending
23	8th Jan-2018	Saeeda Noor D/o Haji Noor Ahmed	Noshki	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	Pending	Yes	Fresh Petition and the reply is still awaiting, still pending before the Hon'ble Ombudsman	Pending
24	8th Jan-2018	Samaira Naz	Panjgur	Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,.	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench.	Pending

25	11th Jan-2018	Taj Muammah Naik Muhammad Ghul Rasool Sons of Ali Jan	Sibi	the Plaintiff was initially filed before the Civil Judge Mach, wherein, the stay Application of the Plaintiff against the building of the school was dismissed after a written reply submitted by the GPE-BEP. Further, the Plaintiff then preferred an Appeal against the Order of the Civil Judge before the District and session judge (Sibi).	Pending	Yes	the matter is still pending.	Pending
26	17th Jan-2018	Ayesha D/o Dostain	Dera Bogti	Complain was submitted before the District and session judge (Sibi) , regarding teacher recruitment.	—	Yes	The Petition has been disposed off on Dated 27th December 2017, in a terms that the matter has to be taken and decided by the District Redressal Committee (DRC)	Disposed off.
27	15-Jan-18	Bibi Saleema D/O Haji Abdul Rehman	Qilla Abdullah	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment as "JVT".	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman as the Contract of the Complainant was already been awarded to the Complainant	Complaint is Disposed of on 07th August 2018, pursuant to the Letter bearing Number 15/2018/PMS/1005-1009, Dated 15th August 2018. The query of the Complainant was resolved	The query of the Complainant was resolved and the Judgment of the Hon'ble Ombudsman received and has been placed in Record	Disposed off
28	1st Mar-2018	Sher Jan S/o Marjan	Zhob	Appeal was submitted before the District and session judge (Zhob) , dispute was over the school site selection.	—	Yes	the matter was resolved between the parties on the terms that the school building will built over the same site selected by the GPE-BEP, through proper site selection mechanism, and the troubling parties were restrained from interfering into the process of building the school.	Resolved.

29	20th Mar-2018	Asma Hussain D/o Nisar Hussain	Sariyab road Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding appointment as J.V teacher..	Pending	Yes	A written reply from the GPE-BEP has been submitted on 20th March 2018, and the disposal of the matter is still pending	Pending
30	29th Mar-2018	Jamila Usman	Panjgur	Petition submitted before Honorable High Court of Balochistan, regarding teacher recruitment,.	Pending	Yes	The Petition is still pending Adjudication before the Hon'ble High Court of Balochistan, at Turbat Bench.	Pending
31	08th March 2018	Ms Rani Kakar D/O Ali Mohammad	Sinjavi, Ziarat	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A thorough written reply from the GPE-BEP has been submitted on 16th May 2018, and the matter was disposed of mainly on the grounds argued in the same reply	Complaint was found to be frivolous and without merit, hence dismissed by the Hon'ble Ombudsman, Balochistan. Complaint is Dismissed on 15th september 2018, pursuant to the Letter bearing Number 195/2018/PMS /1123,-24 Dated 26th September 2018. The Judgment of the Hon'ble Ombudsman received and has been placed in Record	The Complainant was not found to be the competent candidate to teach the children and pursue a career as a teacher	Disposed off

32	6th Apl- 2018	Amina Bibi D/o Bismillah	Dera Allahyar	Complain was submitted before the Hon'ble Provincial Ombudsman (Mohtasib) regional office Naseerabad at DM Jmaali Balochistan, regarding teacher recruitment.	Pending	Yes	Written Reply of the Complaint has been despatched through TCS Courier Dated 06th April 2018, and the outcome of the matter is awaited	Pending
33	11-Apr- 18	Saleeqa sayyad W/O Rafeeullah	Loralai	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment appointment as E. S. T..	A written reply along with its Annexures from the GPE- BEP has been submitted on 31st July 2018, and the Complaint has been disposed off by the Hon'ble Ombudsman mainly on the grounds argued in the same reply	Complaint is Disposed of on 15th August 2018, pursuant to the Letter bearing Number 532/2018/PMS /1020-21, Dated 20th August 2018. The Complaint was dismissed on the grounds that the Complainant had no requisite Associate Degree in Education (ADE) for the post of E.S.T.	The Complaint has been disposed off (Dismissed) by the Hon'ble Ombudsman on the terms that the Applicant has no Associate Degree in Education (ADE), hence the same was dismissed	Disposed off
34	22-Jun- 18	Sadiqa Bibi D/o Abdul Salam	—	Notice has been received from Hon'ble High Court of Balochistan from Sadiqa Bibi, gist of grievance is not mentioned as yet, hearing is on 21st November 018.	The case is pending Before the Hon'ble High Court of Balochistan and is next fixed on 21st November 2018	Yes	—	Pending
35	22-Jun- 18	Kiran Khalid	Quetta	Complain was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP has been submitted on 31st July 2018, and the disposal of the matter is still pending	Pending	Pending	Pending

36	08-Jun-18	Masooda razaq	Baghbana, Khuzdar	Complaint was submitted before the Hon'ble Provincial Ombudsman, Balochistan, Quetta, regarding teacher recruitment.	A written reply from the GPE-BEP has been submitted on 31st July 2018 and the matter was disposed of in directing the Respondents to appoint the Applicant	Complaint is Diisposed of on 04th September 2018, pursuant to the Letter bearing Number 346/2017/PMS /1083-85, Dated 11th September 2018. The Respondents have been directed to appoint the Complainant after completion of all codal formalities to become a JVT	Complaint is allowed and the Judgment of the Hon'ble Ombudsman received and has been placed in Record	Disposed off
----	-----------	---------------	-------------------	--	--	---	---	--------------

## Procurement Grievances

Sr #	Date	Name of the Complainant	Address With Phone Number	Gist of the Complaint	Time fixed for disposal	Whether Complaint redressed or not (Y/N)	If yes the gist of redressed	If rejected Give Reason
1	04-Feb-16	Israr Panezai (CEO) Shaor Org	Quetta 0300-9387204	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. Despite several attempts, the required information on firms behalf, as a result they did not meet eligibility criteria of qualification and thus they were considered as non-responsive.	24-02-16	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committe chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, SHAOR was found to be responsive as per the technical requirements and further allowed to participate in the financial opening.	The grievance is addressed

2	19-Feb-16	Nadir Gul Barhech (CEO) BRSP	Quetta 0812-471437-9	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	As per Grievance Redressal Mechanism, the firm submitted review application to Grievance Redressal Committee at Education Department level. It was re-evaluated in the presence of committee chaired by Special Secretary Education. The firms submitted requisite documents and after re-evaluation, BRSP was found to be responsive as per the technical requirements and further allowed to participate in the financial opening.	The grievance is addressed
3	16-Feb-16	Ahmed Khan Kakar (AM) JV MDF and GRHO	Quetta 0333-7846660	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re-evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ) , Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
4	22-Feb-16	Ihtram Majid (CEO) BRDRS	Quetta 0333-7818478	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ) , Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). BRDRS was found to be responsive as per the technical requirements and further involved in the financial opening.	The grievance is addressed.

5	23-Feb-16	Hameedullah Kakar Youth Org	Quetta 0346-8397898	The firm was disqualified during preliminary evaluation for hiring of Social Mobilization Implementation Partners (SMIPs), due to non-submission of documents or lack of required information, which was required to conduct a proper evaluation of the firm. after multiple attempts to inquire about the required information and lack of response on the firms behalf, they were considered as non-responsive.	24-02-16	Yes	The firm was re evaluated in the presence of Chairman Mr. Zafar Bokhari ( Special Secretary Education ) , Ms,Noureen Iqbal ( Manager Finance) and Mr.Hidayatullah ( S.D.E ). The firm, after thorough re-evaluation was found to be non-responsive as per the stated requirements.	The grievance is addressed.
---	-----------	-----------------------------------	------------------------	---	----------	-----	--	-----------------------------
